
Panahon ng Pagkilos:
Philippine Community
Resilience Project



SUB-MANUAL 7

MONITORING AND EVALUATION

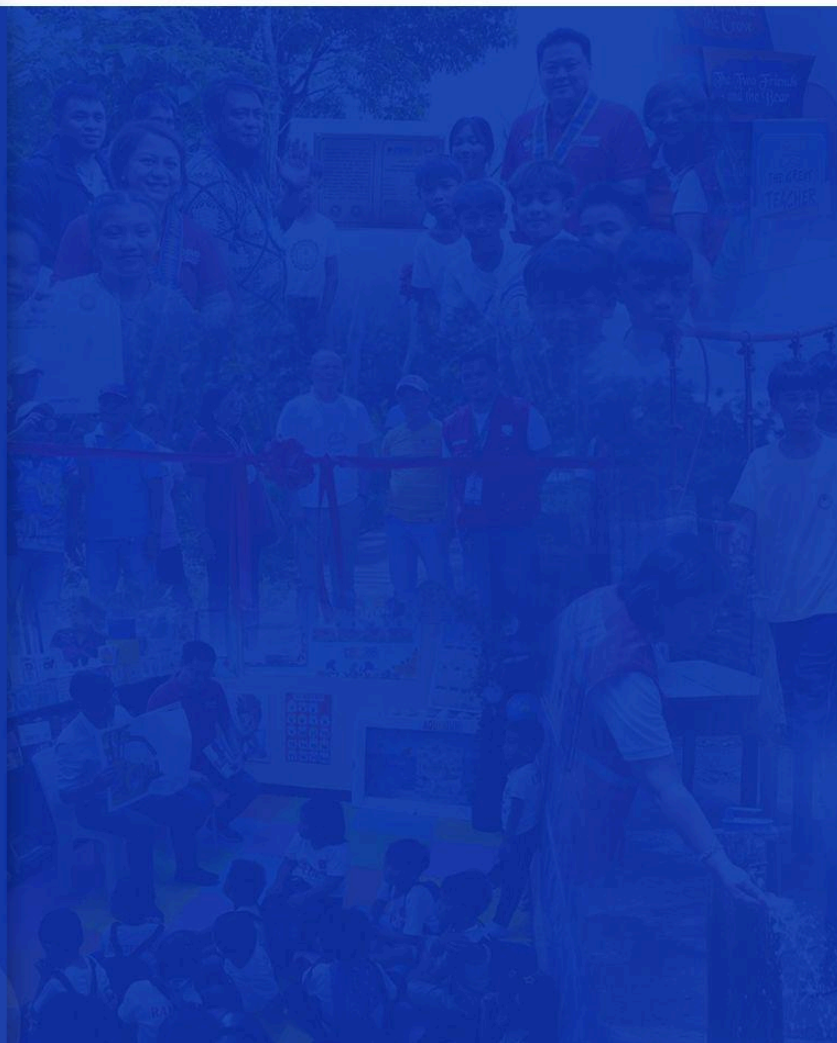

DSWD
Department of Social Welfare and Development

KALAHI CIDSS PAGKILOS

BAGONG PILIPINAS

#BawatBuhayMahalagaSaDSWD

Official Use Only

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF SOCIAL WELFARE AND DEVELOPMENT

PHILIPPINE COMMUNITY RESILIENCE PROJECT (Pagkilos)
[P506594]

SUB-MANUAL 7: MONITORING AND EVALUATION

As of June 2026

Published in 2026 by
Department of Social Welfare and Development
While works of the government are not covered by copyright, this material is an intellectual property of the Department of Social Welfare and Development (DSWD). Proper crediting and attribution to the DSWD is required when using any part or information contained in this material for training and other purposes such as but not limited to research, translation to other formats or languages, and policy development.
As such, the DSWD may also impose fees should this manual be used for commercial purposes. Furthermore, misuse of photos or any part of this material such as posting to social media or developing and publishing new materials, among others, will disrespect and violate the rights of KALAHI-CIDSS staff and compromise the confidentiality and sensitivity of the information on the PCRP and its clients shall be subjected to appropriate sanctions mandated by law.
For Inquiries and other information:
Office Address: DSWD Central Office, Batasan Complex,
Constitution Hills, Quezon City
Telephone Number/s: 8931-8101 to 07 loc. 10121/10117
Fax Number: 8952-0697
E-mail Address: pcrp@dswd.gov.ph
Official Website: pcrp.dswd.gov.ph

Sub-Manual No. 7
MONITORING & EVALUATION

Lead Writers
Mr. Aljay Martinez, Project Development Officer IV - Monitoring and Evaluation
Mr. Jose Zacarias Noel De Castro, Project Development Officer IV - Research

Co-writers
Ms. Didith Bosoen, Deputy National Program Manager for Technical Support
Engr. Bessie Magtangob, Project Development Officer IV - Procurement

World Bank Specialists and Consultants
Ms. Josephine Ramos Jade, Social Development Specialist
Ms. Maria Benilda Redaja, Consultant
Ms. Maria Loreto Padua, Consultant

Official Use Only

ACKNOWLEDGMENT

This sub-manual was developed in fulfillment of the commitments of the Panahon ng Pagkilos: Philippine Community Resilience Project (PCRP) under the Kapit-Bisig Laban sa Kahirapan–Comprehensive and Integrated Delivery of Social Services (KALAHI-CIDSS) Program. It aims to strengthen the implementation of the Monitoring and Evaluation (M&E) system and shall be used in conjunction with the PCRP Project Operations Manual, related sub-manuals, and other M&E instruments and guidelines to ensure the consistent generation, collection, analysis, reporting, and utilization of project information throughout the project cycle.

This sub-manual is the product of the collective efforts of the KALAHI-CIDSS National Program Management Office (NPMO), under the leadership of Atty. Bernadette A. Mapue-Joaquin, RSW, CESO III, and Ms. Didith T. Bosoen. The preparation and technical writing of this sub-manual were led by the M&E Team of the NPMO.

The NPMO likewise acknowledges the invaluable technical guidance and contributions of development partners, regional M&E focal persons, and other technical personnel across the Program, whose expertise and constructive inputs greatly contributed to the development, review, and refinement of this sub-manual.

Official Use Only

TABLE OF CONTENTS

ABBREVIATIONS AND ACRONYMS 4
PART 1: INTRODUCTION 6
1.1. Purpose of the Monitoring and Evaluation (M&E) Sub-Manual 6
1.2. M&E and the Philippine Community Resilience Project (Pagkilos) 6
1.3. Importance of Monitoring and Evaluation in Pagkilos 7
1.4. Continuity and Innovation in M&E Practice 8
1.5. Roles and Responsibilities of M&E Stakeholders 9
1.5.1. Barangay/Community Level 11
1.5.2. Municipal Level 13
1.5.3. Regional Level 14
1.5.4. National Level 16
1.6. Core M&E Principles in PCRP 17
1.7. M&E Through Program Phase 18
PART 2: M&E FRAMEWORK FOR PANAHON NG PAGKILOS 22
2.1. Theory of Change and Results Framework 22
2.2. Implementation 23
2.3. Results 25
2.4. Key Performance Indicators (KPIs) to Measure Community Resilience 26
PART 3: KEY COMPONENTS OF MONITORING AND EVALUATION 27
3.1. Project Monitoring 28
3.1.1. Types of Monitoring: 28
1. Results Monitoring 28
2. Operations Monitoring 29
3. Capacity Building (CapBuild) Monitoring 30
4. Environmental and Social (E&S) Monitoring 30
5. Community Monitoring 31
6. Oversight Monitoring 34
3.2. Evaluation 34
3.2.1 Types and Purposes 34
3.3. Research Agenda 35
3.3.1 Study Protocols and General Procedures 37
3.4 Adherence to the Department's Data Privacy Policy 38
PART 4. M&E IMPLEMENTATION PROCESS 40
4.1. Steps in Implementing M&E 40
Step 1: Understanding the Process, Protocols, and Standards 40
Step 2: Data Collection 41
Step 3: Data Management 44
Step 4: Data Analysis and Expected Outputs 45
Step 5: Data Sharing and Utilization 46
4.2. Organization and Management 47

Official Use Only

4.2.1. Organization 47
ANNEX A: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) THEORY OF CHANGE 52
ANNEX B: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS CHAIN 53
ANNEX C: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS FRAMEWORK 54
ANNEX D: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS MATRIX1 55
ANNEX E: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) INDICATOR TRACKING TABLE (ITT) 60
ANNEX F: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) INDICATOR DOCUMENTATION SHEET1 65
ANNEX G: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) CONTRIBUTIONS TO PHILIPPINE DEVELOPMENT PLAN (PDP) AND SOCIAL PROTECTION PLAN (SPP) 2023–2028 82
ANNEX H: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) CONTRIBUTIONS TO THE NATIONAL ADAPTATION PLAN 2023-2025 88
ANNEX I: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) DATA GATHERING AND REPORTING SCHEDULE BY LEVEL 91
ANNEX J: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) DATA GATHERING ACTIVITIES, SOURCES, AND INFORMATION BY IMPLEMENTATION LEVEL 98
ANNEX K: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) REPORTING FORM REQUIREMENTS 100
ANNEX L: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) COMMUNITY MONITORING TOOLKIT 104
I. Introduction to Community Monitoring in PCRP 104
II. Objectives of Community Monitoring 104
III. Who Participates in Community Monitoring? 104
IV. Activities and Timeline 105
V. Monitoring Plan Template (Sample) 107
VI. Work Plan Template (Sample) 109
VII. Data Gathering Guide (Sample) 110
VIII. Data Analysis & Reporting 111
IX. Barangay Accountability Reporting (BAR) 111
ANNEX M: RESEARCH AND EVALUATION AGENDA 112
ANNEX N: DECLARATION AND DATA CONSENT FORM 118

Official Use Only

ABBREVIATIONS AND ACRONYMS

ACT	Area Coordinating Team
AR	Accountability Reporting
BA	Barangay Assembly
BDC	Barangay Development Council
BDIP	Barangay Development Investment Plan
BDP	Barangay Development Plan
BDRRMC	Barangay Disaster Risk Reduction and Management Committee
CDD	Community-Driven Development
CF	Community Facilitator
CM	Community Monitoring
CSO	Civil Society Organization
DBM	Department of Budget and Management
DEPDEV	Department of Economy, Planning and Development (formerly the National Economic and Development Authority, NEDA)
DILG	Department of the Interior and Local Government
DQA	Data Quality Assessment
HH	Household
HPMES	Harmonized Planning Monitoring and Evaluation System
ICTMS	Information and Communication Technology Management Service
IP	Indigenous People
IS	Information System
ITT	Indicators Tracking Table
KALAHI-CIDSS	Kapit-bisig Laban sa Kahirapan-Comprehensive and Integrated Delivery of Social Services
KPI	Key Performance Indicator
LGU	Local Government Unit
M&E	Monitoring and Evaluation
MAC	Municipal Area Coordinator
MCT	Municipal Coordinating Team
MDE	Municipal Database Encoder
MFA	Municipal Financial Analyst
MIS	Management Information System
MLGU	Municipal Local Government Unit
MOA	Memorandum of Agreement

Official Use Only

MOV	Means of Verification
MResT	Municipal Resilience Team
NPMO	National Project Management Office
O&M	Operation and Maintenance
PCRP	Philippine Community Resilience Project
PDPB	Policy Development and Planning Bureau
PDO	Project Development Objective
PLGU	Provincial Local Government Unit
PSA	Participatory Situation Analysis
RPMO	Regional Project Management Office
SET	Sustainability Evaluation Tool
SFM	Stakeholder Feedback Mechanism
SP	Sub-Project
TA	Technical Assistance
TF	Technical Facilitator
TOC	Theory of Change

Official Use Only

PART 1: INTRODUCTION

1.1. Purpose of the Monitoring and Evaluation (M&E) Sub-Manual

The Monitoring and Evaluation (M&E) Sub-Manual for the *Philippine Community Resilience Project (PCRP), also known as Pagkilos,* serves as a practical and comprehensive guide for carrying out M&E activities that contribute to the project's overarching goal of building resilient and empowered communities.

Designed for program managers, M&E officers and specialists, regional and field staff, local government units (LGUs), community volunteers, and other stakeholders, the manual clarifies M&E roles and responsibilities, outlines data collection and reporting protocols, and promotes a culture of accountability, transparency, and continuous learning throughout all levels of implementation.

1.2. M&E and the Philippine Community Resilience Project (Pagkilos)

The *Philippine Community Resilience Project (Pagkilos-PCRP)* aims to enhance the adaptive capacity of vulnerable communities and ecosystems to natural hazards and emerging risks resulting from Climate Change. This aligns with the Philippine Development Goal to achieve economic and social transformation for a prosperous, inclusive, and resilient society, and is congruent with the Adaptive Shock Responsive Roadmap[1]. Relatedly, the Pagkilos-PCRP is aligned with the country's commitment to the Sustainable Development Goals (SGDs) and will contribute in the following areas:

- SDG 1: No Poverty
- SDG 2: Zero Hunger
- SDG 6: Clean Water and Sanitation
- SDG 8: Decent Work and Economic Growth
- SDG 9: Industry, Innovation, and Infrastructure
- SDG 11: Sustainable Cities and Communities
- SDG 13: Climate Action

Building on the successes and lessons learned from the National Community Driven Development Program (NCDDP) and Vulnerability and Adaptation Manual

[1] As outlined in Chapter 3.2 of the PDP 2023-2028

Official Use Only

(VAM), the Pagkilos will be employing community-based approaches in building resilience among poor households and their communities.

Pagkilos-PCRP targets municipalities whose poverty rates are equal to or higher than the national average of 18.1 percent[2], while also being the most vulnerable based on the following criteria: a.) exposure to environmental and natural hazards[3]; b.) stunting rates among children[4], and; c.) proportion of Indigenous Peoples (IP) in the population[5].

The development objective is to **strengthen community capacities for participatory resilience planning and increase access to resilience investments in vulnerable areas**. This will contribute to the PDP goal to "achieve economic and social transformation for a prosperous, inclusive, and resilient society"[6], and is congruent with the SPP's strategy to implement and operationalize the Adaptive and Shock Responsive Roadmap[7].

To gauge the accomplishment of the development objective, the following Key Performance Indicators (KPIs) will be used:

a. Percentage of beneficiaries reporting that they can influence community resilience planning;
b. Percentage of target municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP); and
c. Population in target areas benefiting from resilience investments.

Several intermediate indicators have been identified as directly contributing to the accomplishment of the development objective KPIs.

1.3. Importance of Monitoring and Evaluation in Pagkilos

As a Community-Driven Development (CDD) initiative, Pagkilos relies on a strong M&E system to ensure effective implementation, community ownership, and

[2] Based on the 2021 data from the Philippine Statistics Authority (PSA)
[3] Assessed based on six key environmental/natural hazards as identified in the National Adaptation Plan - Philippines, namely - drought, heat, landslide, storm, flood and coastal inundation.
[4] Stunting rates as identified through the 2023 Operation Timbang (OPT) program, a community-based annual nutrition assessment conducted by the DOH
[5] The National Adaptation Plan identified Indigenous Peoples as among the most vulnerable sectors to climate change.
[6] As discussed in Chapter 1 of PDP 2023-2028
[7] As discussed in Chapter 3.2 of PDP 2023-2028

Official Use Only

achievement of targeted resilience outcomes.[8] The M&E framework enables adaptive management by tracking progress, generating timely data, informing strategic decisions, and promoting inclusive participation.[9]

Key M&E functions in Pagkilos include:

- *Tracking Progress and Results*: M&E provides real-time, reliable data on project activities and outcomes, measuring achievements in access to resilience services, disaster preparedness, social inclusion, and institutional strengthening.
- *Data-Driven Decision-Making*: M&E supports evidence-based adjustments by identifying what works and guiding the reallocation of resources to maximize impact.
- *Accountability and Transparency*: M&E reinforces public trust through regular reporting, community feedback loops, and documentation of resource use and project achievements.
- *Learning and Knowledge Sharing*: The system captures lessons learned, supports replication of successful approaches, and enables continuous improvement.
- *Compliance with Safeguards and Standards*: M&E ensures adherence to technical standards, environmental and social safeguards, and principles of inclusivity—especially for Indigenous Peoples (IPs) and other marginalized groups.
- *Adaptive Management*: M&E empowers implementers to make informed adjustments in response to emerging community needs, climate shocks, and socio-political changes.

1.4. Continuity and Innovation in M&E Practice

Pagkilos builds on the foundations laid by the National Community-Driven Development Program (NCDDP) and its Additional Financing (AF). The NCDDP and NCDDP AF had institutionalized participatory M&E systems, implemented

[8] World Bank. (2013). *Community-driven development toolkit: Governance and accountability dimensions*. Washington, DC: World Bank.
[9] Bours, D., McGinn, C., & Pringle, P. (2014). *Monitoring & evaluation for climate change adaptation and resilience: A synthesis of tools, frameworks and approaches*. SEA Change Community of Practice & UKCIP.

Official Use Only

results-based frameworks, and integrated social and environmental safeguards[10].

Lessons learned from predecessor modalities were integrated in the development of the project's new Management Information System (MIS). Similar to the previous MIS systems - the Geotagging Web Application (GTWA) and the Project Information Management System (PIMS) - the new MIS will be where data is encoded from paper-based forms from the field. These data, in turn, are consolidated and reviewed to be used as reference in reports and decisions-made.

The new MIS will be developed with continuity and system sustainability in mind - being built from open source software. Additionally, the new MIS will innovate from previous systems by providing an enhanced dashboard, improved custom report generation, use of AI and other tools (maps, calendar, etc.). The more feature-rich management information hopes to enhance project implementation and outcomes through:

- Deepening community involvement in adaptive resilience planning;
- Linking daily implementation to broader development outcomes in resilience
- Integrating key focus areas of Adaptive and Shock-Responsive Social Protection (ASRSP).
- Expanding the use of science-based, real-time data to support strategic decisions[11]

Additionally, the new MIS will promote the integration of M&E and Knowledge Management. The project's management information system is designed to be useful tools for analysis and feedback at all levels - community, municipal, regional, and national levels. These feedback loops will enable the use of data as actionable insight - promoting the transformation of tacit knowledge into explicit knowledge (*see SM 9: Capacity Building under Knowledge Management section)*

1.5. Roles and Responsibilities of M&E Stakeholders

Effectiveness of the Pagkilos-PCRP Monitoring and Evaluation (M&E) is contingent on the accurate, coordinated, and timely fulfillment of responsibilities among stakeholders at the barangay, municipal, regional, and national levels.

[10] National Economic and Development Authority (NEDA). (2015). *National Community-Driven Development Program (NCDDP) Project Design Document.* Quezon City: NEDA.
[11] Social Protection and Labor (SPL). (2020). *Adaptive Social Protection and Shock-Responsive Social Protection Programs: A Framework.* Manila: DSWD.

Official Use Only

Table 1: M&E Stakeholders and Responsibilities

Level	M&E Stakeholders	Roles/Responsibilities
National	National Program Management Office (NPMO)	Leads M&E design, manages databases, oversees data quality, and consolidates findings to inform national policy.
Regional	Regional Program Management Offices (RPMOs)	Provide field guidance, technical assistance, and quality assurance.
Municipal	Area Coordinating Teams (ACTs)	Conduct community-level data collection, validation, and training.
	Local Government Units (LGUs)	Integrate monitoring data into local planning, budgeting, and service delivery.
Barangay / Community	Community Volunteers and IP Representatives	Ensure grassroots perspectives and priorities are reflected in M&E processes.
	Civil Society Organizations (CSOs) and Partners	Offer third-party validation and promote accountability through independent monitoring.

The NPMO management is in charge of policy formulation and decision-making. As a result, they will be held accountable for strategic planning and achieving overall program impact or project development goals and outcomes. The NPMO reports to DSWD as a parent institution.

On the other hand, the RPMO and program managers are held accountable for policy implementation and program management. They interpret the aggregated outputs and connect them to the program's goals.


Technical, operations and support staff at the barangay/community, and municipal levels are held accountable for assuring the quality of project activity execution, which includes training reports, paper-based forms, pictures, encoded data in management information systems, and technical analysis. They are mainly responsible for the accuracy of community data and the interpretation of

Official Use Only

activities/inputs.[12]

Refer to Annex I for the tabular breakdown of Data Gathering and Reporting Schedule by Level.

Figure 1: Management Levels and Functional Roles

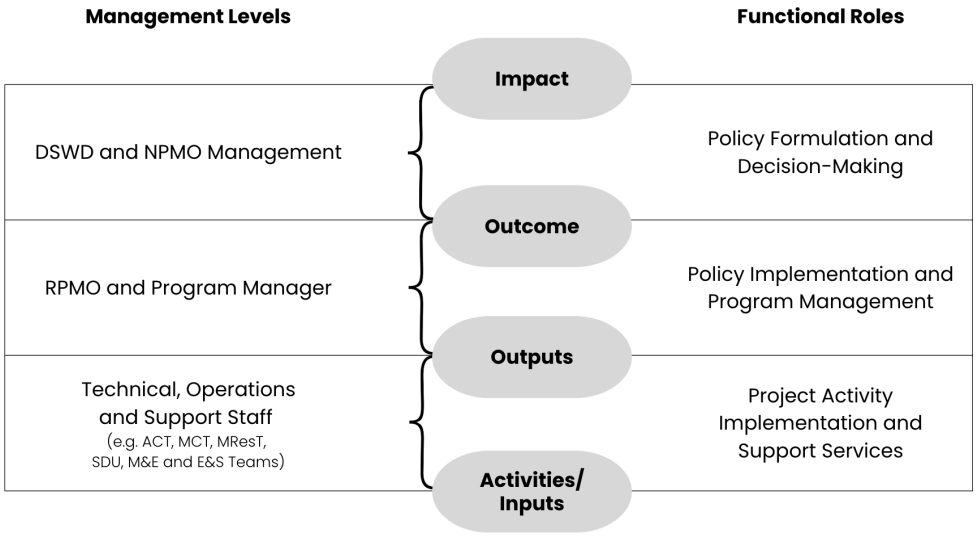

1.5.1. Barangay/Community Level

Data gathered at the community-level are gathered by Community-Volunteers (CV) in coordination with Barangay Officials, and with assistance from the Area/Municipal Coordinating Teams (ACT/MCT). This community-level data will provide the community to establish baselines, track progress, identify discrepancies, and ensure that resources are being used effectively and for their intended purpose.

Members of the Barangay Resilience Team (BResT), composed of representatives from various sitios/puroks and sectors, select from among their ranks those who will serve as members of the Community Monitoring Sub-Committee (CMSC). The CMSC oversees and monitors the implementation of the sub-project. To do so, they are to facilitate the preparation of the Community Monitoring Plans with assistance from the ACT and MCT. This plan identifies the key areas to be monitored, and CMSC will define specific and measurable indicators to track progress and identify potential issues. From this, two reports are to be submitted within seven days of the barangay orientation:

[12] USAID. (2016). *Project Management and Monitoring & Evaluation Guide: Roles and Responsibilities*. United States Agency for International Development.

Official Use Only

Community Monitoring Plan	:	Identifies key areas to be monitored and defines measurable indicators. Additionally, this plan establishes monitoring schedules and responsibilities
Barangay Profile	:	Captures data on the barangay's demographics, socio-economic conditions, infrastructure, governance, etc.

To ensure that the community monitoring process is systematic and well-documented, the project makes use of standardized tools and protocols. These tools support the collection, verification, and reporting of data and activities related to sub-project implementation.

One of the key references for documentation is the *Compendium of Forms*, which consolidates all standardized forms used throughout the project. These forms establish a clear and traceable record of actions, decisions, and requests made during implementation, thereby promoting transparency and accountability across all levels.

Building on this, *Data Collection and Documentation of Activities* requires the timely completion of applicable forms by responsible Community Volunteers (CVs). Each form type corresponds to a specific area of implementation and is filled out with technical support from the appropriate staff:

- Technical Facilitator (TF) – Engineering Forms
- Municipal Financial Analyst (MFA) – Financial Forms
- Community Facilitator (CEF) and Area Coordinator (AC) – Process Forms
- ACT/MCT – Procurement Forms

To maintain timely reporting, these forms must be submitted within three days of the conduct of the activity.

In addition to the standardized forms, documentation is further strengthened through the submission of *Means of Verification (MOVs)*. These are supplementary documents—such as barangay resolutions, geotagged photos, or attendance sheets—that validate the completion of deliverables and activities. MOVs provide additional assurance of compliance and are required within five days after each activity. To uphold the integrity of submitted documents, each set

Official Use Only

of MOVs undergoes a Quality Review within two days to ensure consistency with the corresponding forms from the Compendium.

Moving from documentation to monitoring, *Geotagging and Monitoring of Sub-Projects (SPs)* play a critical role in verifying physical progress. Relevant SP forms and geotagged photos are submitted as visual and documentary evidence of SP status, materials used, and work quality. These are essential references for the National and Regional Program Management Offices (NPMO/RPMO) as they supervise and monitor implementation across communities.

Moreover, geotagged photos also serve as "*Proof of Progress*" and are required attachments to the Request for Fund Release (RFR), which is prepared by the Community Sub-Project Management Committee (CSPMC). The approval of fund releases for subsequent tranches depends on documented evidence—collected through M&E processes—that the previous funds were utilized properly and that the SP is progressing in accordance with the approved work plan.

Finally, to ensure both financial and technical accountability, the *Review of Community-Prepared Technical and Financial Records* is conducted by CVs, TFs, and MFAs. These reviews confirm that sub-projects are compliant with established standards, that funds are properly managed, and that implementation is aligned with agreed objectives. Reviews are scheduled either monthly or within seven days after the conduct of related activities, depending on the type of record involved.

1.5.2. Municipal Level

Data from the various barangays are verified and consolidated at the Municipal Level. This is made possible by the Data Sharing Agreement (DSA)[13] and Memorandum of Agreement (MOA) between the DSWD and LGU that is prepared at the start of the project engagement. These legal agreements allow for the establishment of institutional arrangements for data sharing and systems set-up. The Area Coordinating Teams (ACTs) lead the preparation and facilitation of the approval of the DSA and MOA in their assigned municipality.

Communities submit their accomplished forms and corresponding MOVs to the ACTs and Municipal Coordinating Teams (MCTs) for consolidation, encoding, and verification - as detailed below:

[13] Kindly refer to Memorandum Circular No. 03 s. 2026 entitled *'Enhanced Data Privacy Manual'*

Official Use Only

1. *Quality Assurance of Barangay Submissions*
    - ACTs and MCTs check the submissions in terms of Quality, Quantity and Timeliness, and details their feedback in a report on the Inventory and Assessment of MOVs
2. *Encoding of Paper-Based Forms* and *Scanning and Digitizing of Reports*
    - The Municipal Data Analyst (MDE) and Project Evaluation Assistant (PEA) are responsible for the encoding of the paper-based reports into the Management Information System (MIS). Paper-based reports are to be encoded within three (3) days of receipt.
    - To safeguard project documents, digital copies of reports/forms and MOVs are to be made and uploaded into the MIS. An inventory of scanned MOVs is to be prepared by the MDE and PEA. This is to be completed within one (1) day after receipt of the MOV.
3. *Verification and approval of encoded KPI data in the MIS*
    - The TF and MFA review the accuracy and completeness of the data encoded in the MIS, with the final approval being provided by the AC and MC. The verification and approval is to be conducted within two days of encoding.

As focals for the MIS, the MDE and PEA will be involved in capacity building activities that will help them in the performance of their duties. Relatedly, they will assist the technical staff in the ACT and MCT in the operation of the MIS and implementation of the data collection system.

At the end of the project cycle, the ACT and MCT will work closely with the Municipal Resilience Team (MResT), Municipal Planning and Development Coordinator (MPDO), and the Local Social Welfare and Development Officer (LSWDO) in turning over reports and records to the LGU as well as securing the report acceptance certificate.

1.5.3. Regional Level

The Regional Project Management Office (RPMO) serves as the primary operational hub and implementing arm at the regional level. It acts as the crucial link between national directives (policy implementation) and grassroot implementation by the ACTs/MCTs and communities (program management).

When national deadlines are set by the NPMO, the RPMO plans and schedules its activities and cascades its own deadlines to the ACT/MCTs accordingly. The RPMO

Official Use Only

is expected to closely coordinate with the ACTs, and as part of its supervisory function, provide guidance and assistance for concerns that may be raised.

The regional M&E manages the MIS at the regional level. They ensure data is encoded within the deadline set by the region, to meet national reporting deadlines. Relatedly, the RPMO ensures concerns and realities at the ground level (when they affect project implementation) are documented in the narrative reports submitted by the ACT. The RPMO consolidates and summarizes the reports from the ACT in their report submitted to the NPMO.

To ensure the reliability, completeness, and timeliness of data collected, the RPMO will routinely conduct systematic reviews through Data Quality Assessments (DQAs) to check for potential errors, inconsistencies, and gaps in the data as they are collected, processed, and archived in the communities or with the ACTs and MCTs.

Table 2: Overview of M&E Functions of the RPMO

Area	Responsibilities
Strategic and System Oversight	• Accountable for policy implementation and program management; • Provides field guidance, TA, and quality assurance; • Ensures compliance with program processes and directives cascaded by the NPMO; • Supervises field staff (ACT)
Monitoring, Analysis and Data Integrity	• Consolidates reports from the municipalities; • Verifies, checks and approves data uploaded in the MIS; • Endorses concerns requiring involvement of the NPMO
Reporting and Information Utilization	• Generates and processes KPI, technical and financial data from the MIS to calculate progress, identify trends, and compare performance for regional reports • Submits regular reports to the NPMO, PDPB, and other regional stakeholders and oversight agencies. • Updates the NPMO on the situations from the field vis-a-vis its accomplishments, and provides data-informed recommendations.

Official Use Only

1.5.4. National Level

The National Program Management Office (NPMO) is responsible for the overall management, coordination, technical assistance and strategic direction of the M&E system at the national level. In accordance with the intended project outcomes and committed targets, it designs, plans, and schedules the conduct of M&E activities - this includes but is not limited to regional and municipal targets and deadlines (in accordance with the overall indicator tracking table), deadlines for encoding, and initiatives and possible steering measures.

Relatedly, it designs and maintains the overall MIS. It cascades policies and protocols to be observed to ensure that data encoded are accurate and valid. Part of the National M&E is to routinely check for inconsistencies, errors, and discrepancies within the data. This may involve cross-referencing information with MOVs and inventories submitted, comparing data against targets and guidelines, and ensures adherence to established protocols.

Official data is used to generate meaningful insight for national reports and to be shared with relevant stakeholders. M&E serves a crucial role in ensuring the availability, quality, and truthfulness of data to be reported officially, as well as analyzing and making sense of it when presented and/or reported when: 1.) the National Steering Committee (NSC) for KALAHI-CIDSS is convened; 2.) reported to the World Bank to gauge the progress of commitments in the loan covenant; 3.) reported to interested development partners (e.g. NGOs/CSOs, Academe, etc.); 4.) reported to oversight National Agencies (e.g. COA, DBM), and 5.) reported and consolidated to gauge the progress of National Plans and International Commitments in which PAGKILOS-PCRP is intended to contribute towards.

Steering measures such as the provision of targeted Technical Assistance (TAs) and Capacity Building Activities for RPMOs identified requiring interventions may also be initiated by the NPMO. Additionally, PAGKILOS-PCRP has six (6) identified priority evaluation studies. This is to be led by the NPMO and coordinated with either all or select RPMOs (depending on the scope of the study) who will assist in field works or as directed.

Official Use Only

Table 3: Overview of the M&E Functions of the NPMO

Area	Responsibilities
Strategic and System Oversight	• Initiates the design and planning of M&E Activities • Manages the MIS at the national level • Provides Technical Assistance to RPMOs
Monitoring, Analysis and Data Integrity	• Overall Results Monitoring • Periodically assess KPIs to determine if they are being met and whether steering measures are needed
Reporting and Information Utilization	• Leads the conduct of research studies • Prepares comprehensive reports on the program's progress, performance, and impact. • Submits regular reports to the NSC, WB, DBM, COA and other stakeholders/oversight agencies.

1.6. Core M&E Principles in PCRP

PCRP's M&E system is built on the following guiding principles:

Table 4: Pagkilos Core M&E Principles

P	Participatory Monitoring and Evaluation	Broaden community participation in monitoring and evaluation processes, ensuring that marginalized groups (e.g., women, indigenous peoples, persons with disabilities, senior citizens) are actively involved in assessing interventions, outcomes, and impact.
A	Adaptive M&E for Resilience	Design M&E systems that enable communities to learn from results and adjust programs and practices to improve resilience outcomes, using real-time data and feedback loops for continuous improvement.
G	Good Governance in M&E	Embed transparency, accountability, and inclusion in M&E practices through participatory monitoring tools (e.g., community scorecards), stakeholder feedback mechanisms, and public disclosure of findings.
K	Knowledge Building through M&E	Systematically gather, analyze, and disseminate data and learning products to deepen the understanding of differentiated risks, community adaptation practices, and innovation pathways.
I	Intergovernmental Collaboration in M&E	Promote coordinated M&E approaches across government agencies and LGUs, incentivizing joint monitoring activities, shared data systems, and

Official Use Only

		convergence in resilience-building efforts.
L	Localized and Flexible M&E Systems	Develop M&E systems that are community-based, adaptable to local conditions, and support social accountability through participatory monitoring of financial management, procurement, and resilience activities.
O	Organizational Development for M&E Capacity	Invest in strengthening the capacities of local organizations, action teams, and LGUs to design, implement, analyze, and use M&E processes sustainably.
S	Science-Based M&E for Decision-Making	Use evidence-based methods and rigorous data analysis to support rational, prioritized, and adaptive decision-making in program planning, resource allocation, and policy advocacy.


1.7. M&E Through Program Phase

The Pagkilos-PCRP adopts a Monitoring and Evaluation (M&E) system that is fully embedded across all phases of the project cycle — from pre-implementation through implementation and post-implementation to closure. Integrating M&E processes at every stage ensures that project managers, implementers, and partners have timely, reliable information to guide evidence-based decision-making, adaptive management, and strategic adjustments.

Managing results requires more than tracking outputs and activities; it demands a system where M&E findings meaningfully inform project operations and organizational learning. To support this, the design and planning of M&E activities are initiated by the National Project Management Office (NPMO) and further operationalized through the Regional Project Management Offices (RPMOs). Monitoring and evaluation efforts are conducted at multiple levels — national, regional, municipal, and community — ensuring a comprehensive, participatory, and multilevel approach to project performance management. Figure xx below illustrates how the M&E system supports each phase of the project cycle.

Official Use Only

Figure 2: M&E Through Program Phase

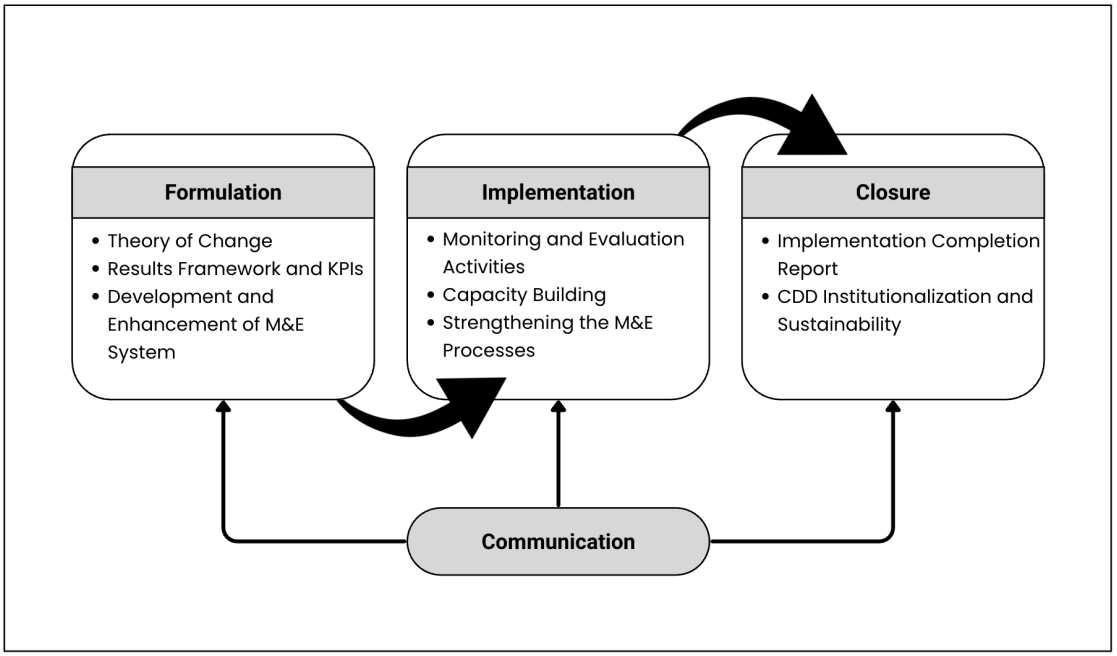

Consistent with previous implementations of the Community-Driven Development (CDD) approach, the Pagkilos' M&E activities are structured not only to measure performance but also to promote continuous learning and adaptation. M&E outputs help sharpen stakeholders' understanding of field realities, enabling operational policies, systems, and strategies to be continuously improved based on emerging evidence.

Responsibilities for M&E are clearly distributed across levels of implementation:

- At the national and regional levels, designated M&E staff coordinate activities, provide Technical Assistance (TA) to the Area Coordinating Teams (ACTs) and Municipal Resilience Teams (MResTs), oversee training on M&E tools and methods, manage encoding and data consolidation, conduct regular data quality reviews, and monitor project performance.

- At the municipal and barangay levels, ACTs, MResTs, and community volunteers participate directly in data collection, local monitoring, feedback generation, and participatory validation processes.

The table below illustrates the distribution of major M&E activities across the three key phases of the project cycle:

Official Use Only

Table 5: M&E Across the Project

Major M&E Activities	Pre-Implementation	Social Preparation	Sub-project Implementation
Management Information System	Database Enhancement	System Maintenance Data Sharing and Coordination with ICTMS and other OBSUs	
Staff Capacity Building	RPMO and ACT Training on M&E Tools	Technical Assistance and Regular Learning Sessions	
LGU and Community Capacity Building	MCT, MDE, other LGUs and Community Volunteers Training on M&E Tools	Community Skills Training	
		Technical Assistance and Regular Learning Sessions	
Results Monitoring	Comprehensive M&E Plan Development	Monitoring of KPIs Through Indicators Tracking Table (ITT) and Quarterly Reporting	
Operations Monitoring	Guidelines Review and Enhancement	Tracking of Activities and Physical Accomplishment; Data Gathering, Checking, Submission, Reporting and Data Sharing	
Geographic Information System	Geotagging Review and Enhancement	Participatory Mapping; Geotagging of Proposed Sites	Geotagging of Ongoing Sub-project Implementation
Community Monitoring	CM Orientation and Selection of Volunteers	Preparation of CM Plans	
Stakeholder Feedback Mechanism	Review and Enhancement of SFM per EODB	SFM Orientation; Installation; and Selection of Volunteers	Stakeholder Feedback Monitoring (SFM)
Data Analysis	Data Gathering	Data Preparation	Data Processing and Analysis
Data Quality Assessment	Review and Enhancement of DQA	DQA in All Municipalities (twice a year)	
Internal Evaluation; PREW; Special Studies	Guidelines Review and Enhancement	Data Gathering and Survey	Report Preparation and Feedbacking

Official Use Only

External Evaluation, Special Studies	Review Existing DSWD Research and Evaluation Guide	Provision of Support to Evaluators as Needed	
Progress Report	Preparation of Report Template		Monthly/ Quarterly/ Annual Progress Report; In-sync with Other DSWD OBSUs and NGAs Report Requirement; Implementation Completion Report

Pagkilos staff at all levels are encouraged to use this as a reference guide for understanding the expected monitoring and evaluation activities throughout the project cycle, ensuring clarity of roles, timelines, and deliverables.

Official Use Only

PART 2: M&E FRAMEWORK FOR PANAHON NG PAGKILOS

2.1. Theory of Change and Results Framework

The M&E Framework is designed to track, evaluate, and facilitate learning on how project inputs and activities contribute to building resilient and empowered communities. It is best understood through its *Theory of Change (see Annex A)* which visualizes the determined causal relationship between the project's intended outcomes and the actions the project and its implementers are programmed to take.

The *Theory of Change* is best understood as a tiered relationship mapping the causal pathways that converts inputs and activities, to intermediate outcomes, end of program outcomes, as well as the project's to broader national plans and international commitments.

At its base level, inputs consist of the: 1.) Financial Resources; 2.) Human Resources; 3.) Training modules and tools; 4.) Data systems and digital tools; 5.) Community mobilization tools; 4.) Technical Assistance; and Logistical Support. These are best understood as what is functionally necessary to conduct the next tier of inputs.

Foundational activities are requisite tasks for project implementation such as the development of manuals, and the information system, identifying who and where should the targets be, defining the organizational structure, providing training and capacity building to have the necessary competencies among project personnel, etc.

These foundational activities are preceded by other activities oriented towards preparing for the roll-out of the project such as LGU enrollment, media briefings, mapping of service providers, inter-program convergence activities, inter-agency partnerships, and other partnership building activities.

Subsequently, these activities are followed by actual project implementation activities as programs in the four components of the Pagkilos. There are output level Key Performance Indicators (KPIs) for select activities - those specifically identified to contribute to intermediate outcomes, and can serve to gauge the


Official Use Only

overall performance of the project.

As shown in the ToC visualization, there are causal links between activities being conducted and behavioral outcomes intended by the project - as well as how these behavioral changes will, over time, contribute to the accomplishment of higher level broader goals (impact).

The Results Framework (RF) is a simplified version of the Theory of Change. Whereas the ToC comprehensively illustrates the causal pathways, the RF is a more focused, linear tool which visually summarizes the project's strategic objectives in terms of inputs, outputs, and outcomes, etc.

Figure 3: Pagkilos Results Framework

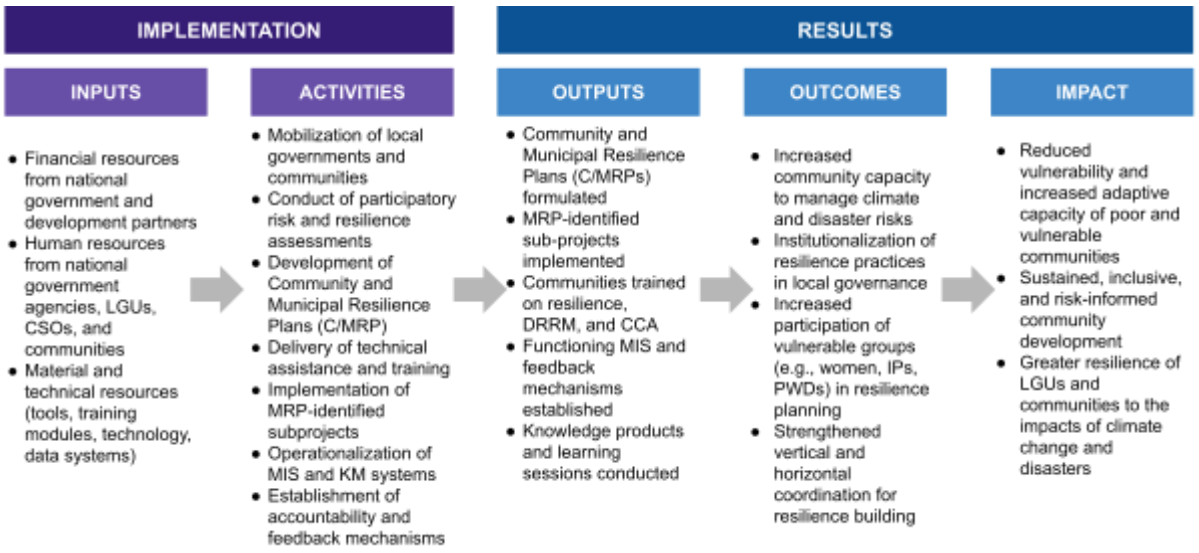

2.2. Implementation

Implementation refers to the conversion of 'inputs' (e.g. financial, human, and material resources) through various project activities into 'outputs' which contribute to the accomplishment of intended project outcomes (as defined through the indicators) and eventually making an impact (addressing the need/vulnerability that created the project in the first place)

Pagkilos is structured in accordance with the three types of inputs, and a contingency measure - and these comprise the four components of the project.

Component 1: Community Grants for Resilience Planning and Investment
Component 2: Institutional Support for Local Resilience

Official Use Only

Component 3: Project Monitoring, Evaluation and Management
Component 4: Contingent Emergency Response Component

Component 1: *Community Grants for Resilient Planning and Investment* involves the conduct of community planning exercises at the barangay whose insights would be integrated into the three year municipal resilience plan (Subcomponent 1.1 - Community Planning Grants). This plan identifies priority community-based sub projects to be funded by the PCRP (under Subcomponent 1.2 - Community Grants for Resilience Investment).

Each participating municipality will be allocated an indicative grant of PHP 50 to 70 million to implement a three-year resilience plan[14], and a 20% Local Counterpart Contribution (LCC) will be required in cash or in kind as support to the project. The general categories of sub projects that may be implemented are:

a. Resilient basic services and facilities essential to the survival and safety of communities (e.g. health facilities, water and sanitation systems, etc.)
b. Support for resilient economic/livelihood activities (e.g. pre- and post-harvest facilities, drainage and small scale irrigation, capacity building for livelihood activities, etc.)
c. Environmental protection and preservation (e.g. slope protection, etc.)
d. Strengthening community-municipal network for resilience (e.g. early detection mechanisms, etc.)

Component 2: *Institutional Support for Local Resilience* involves the recruitment and capacity building of national and sub-national project staff, orientation-training of key partner agencies at all levels, establishment of a knowledge exchange platform on resilience, and the development/updating of project manuals/submanuals.

Component 3: *Project Monitoring and Management* covers the cost of Program Management (Sub-component 3.1) and Monitoring and Evaluation

[14] Each participating municipality will be allocated an indicative grant of Php50 million to Php70 million to implement a three-year resilience plan. The grant will be differentiated based on the income class of the municipality: i.e., 1st to 3rd class municipalities will be allocated a maximum grant of Php50 Million while 4th to 6th class municipalities will have a Php70 Million allocation. Actual grant will depend on the appraisal and approval of the PCRP Regional Team or the National Team, depending on the complexity and cost of the sub-project

Official Use Only

(Sub-component 3.2). The former will fund the creation of a National Program Management Office (NPMO) at the DSWD Central Office, and 16 Regional Project Management Offices (RPMOs). Program Management (3.1) would also cover the operational costs and activities of the NPMO and RPMO such as the conduct of planning, budgeting, and capacity building activities, as well as social marketing, coordination, partnership development, etc.

Component 4: Contingent Emergency Response will serve as a proactive mechanism that could be activated for the rapid mobilization of financing to respond to an eligible crisis or emergency. This component would allow for rapid reallocation of uncommitted project funds towards urgent needs in the event of a disaster that may include typhoons, floods, earthquakes, volcanic eruptions, droughts, and disease outbreaks. The implementation of the CERC will be triggered by the declaration of a State of Calamity by the mandated national or subnational authority or a State of Public Health Emergency

2.3. Results

Each office, division, section, and staff - from the national to the ACT, and by extension to the Community Volunteers (CVs) - contributes to overall results/ accomplishments of the project. Similarly, each activity, whether implemented by the CRIP, a capacity building activity, and/or provision of Technical Assistance, should contribute to the overall accomplishment of the project's development objective.

Key Performance Indicators (KPIs), as previously mentioned, gauge the performance of the program and its output indicators reflect immediate results of activities conducted. At the most basic level, these serve to measure how much has been achieved. Each implementing level (RPMO, Municipality, and ACT/MCT) has a share (quota) that comprise the overall national targets set by the NPMO. The aim is to meet the numerical target within the proper timeframe.

Annex D shows the Results Matrix wherein one can find the numerical target for each indicator for a certain year. Each implementing level's share by indicator is determined by the batch schedules. An RPMOs share is determined by the number of Batch 1 and 2 municipalities they will be implementing for a certain year. Annex

Official Use Only

C shows the Indicator Tracking Table, and will serve as the reporting template for tracking KPI accomplishment at the Region and National levels.

The progressive accomplishment of KPIs (results monitoring) is primarily reported through the following regular reports.

Table 6: Primary Reports Monitoring

Frequency	Report
Monthly	KPI Status Report ODA Status Report
Quarterly	DepDev Alert Mechanism World Bank report GAD Report
Annual	ODA Annual Portfolio Review KALAHI-CIDDS Annual Report
End of Project	Impact Evaluation (IE) Implementation Completion Report (ICR)

2.4. Key Performance Indicators (KPIs) to Measure Community Resilience

The Pagkilos has three Project Development Output Indicators that contribute to the accomplishment of the Project Development Objective which is to *'strengthen community capacities for participatory resilience planning and increase resilience investments in vulnerable areas'*. These are as follows:

- Beneficiaries reporting that they can influence community resilience planning.
- Municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP)
- Population in target areas benefiting from resilience investments

The abovementioned indicators are made possible through the accomplishment of the intermediate indicators.

A. Community Resilience

Official Use Only

1. Communities trained on risk and vulnerability assessment; and, resilience planning
2. Household participation in barangay assemblies for community resilience planning
3. Investments in accordance with relevant national guidelines for resilience
4. Municipalities that had PLGU participation in the municipal-community resilience planning.
5. Sub-projects completed in accordance with approved technical plans and budget
6. Sub-projects with sustainability rating that is satisfactory or higher
7. Sub-projects with O&M plans with allocated annual budget
8. Female participation in paid community labor
9. Municipalities with at least 40 percent women's representation in Municipal Resilience Teams (MResTs), with 30% (of the 40% women members) occupying/performing leadership roles.
10. Women leaders in Municipal Resilience Teams and Barangay Development Councils reporting meaningful involvement in decision-making processes

B. Institutional Support for Local Resilience

1. Municipalities with enhanced capabilities on risk and vulnerability assessment; and, resilience planning
2. Knowledge portal developed and installed
3. Municipalities with institutionalized Municipal Resilience Teams
4. Trained project staff at national and regional levels

C. Project Management and Monitoring and Evaluation

1. Grievances received that are addressed

PART 3: KEY COMPONENTS OF MONITORING AND EVALUATION

Monitoring and Evaluation (M&E) are critical functions of the Pagkilos that ensure project accountability, effectiveness, and learning. While both processes are complementary, they serve distinct purposes and are implemented through different approaches.

Official Use Only

3.1. Project Monitoring

Project monitoring is the systematic and continuous process of collecting, analyzing, and using information to track the progress of project implementation. Its primary objectives are to:

- Ensure that project activities are implemented as planned.
- Track the achievement of expected outputs and outcomes.
- Provide timely feedback for decision-making and adaptive management.
- Support accountability to stakeholders, including communities, LGUs, and donors.

This is also in keeping with the duties and responsibilities of the Philippine Government, through the department, in its loan covenant for the Project which requires the KALAHI-CIDSS to *maintain policies and procedures adequate for monitoring and evaluation of indicators, progress of SPs, and achievement of project objectives.*

Project Monitoring is also a shared responsibility between the RPMO and Local Government Unit (LGU) at the level of the Municipality, as well as with Provincial Government for tripartite agreements. The Memorandum of Agreement (MOA) provides provisions authorizing the department to conduct monitoring and evaluation activities for the project which includes but not limited to the collection of data during project activities or in accordance to project needs[15]. The MOA also provides for the participation of the LGU in the strategic monitoring of SPs[16]. These arrangements may further be detailed in Specific Implementation Arrangement (SIA) following the signed MOA, but generally, project monitoring at the local level should be compliant with the provisions in the POM, M&E Manual, and other sub-manuals.

3.1.1. Types of Monitoring:

1. **Results Monitoring**

   Results Monitoring is designed to address the "so what" question by

[15] Section 4.2 of the Memorandum of Agreement (MOA) template attached as Annex 4 of the POM
[16] Section 4.3 of the draft Memorandum of Agreement (MOA) template attached as Annex 4 of the POM

Official Use Only

measuring and reporting whether program implementation is progressing at the right pace and direction toward achieving the Project Development Objective (PDO). It is a continuous process of collecting and analyzing information to compare how well a project, program, or policy is being implemented against expected results. As such, results monitoring provides a comprehensive evaluation of progress and performance over time.

Given its program-wide scope, the analysis is primarily conducted at the national level by Program Managers, with support from reports generated by the Regional Project Management Offices (RPMOs). Guided by the Theory of Change (TOC) and Results Framework, M&E Officers periodically assess outcome-level key performance indicators (KPIs) to determine if these are being met. In tracking results, the means of verification (MOVs) are used, as identified in subsequent sections, and processed through the database system, which automatically generates data on the KPIs. Data collected is routinely compared against barangay and municipal baseline information and complemented by special studies, as further discussed in the Evaluation section.

2. Operations Monitoring

Operations Monitoring focuses on ensuring compliance by answering the question, "Did they do it?" This involves tracking whether project activities are being executed according to approved work plans, operational guidelines, schedules, policies, and standards, with clear responsibility assigned to specific units at each stage of implementation. Operations monitoring ensures that the project's fidelity is maintained throughout, verifying that activities are being carried out as intended.

This type of monitoring also includes assessing the utilization of resources, monitoring adherence to timelines, procurement processes, and ensuring financial compliance at every phase of the project. Specifically, operations monitoring addresses the technical management of key areas, including:

- *Community Processes*: Ensuring that community engagement follows the planned approach within the community resilience implementation process;

Official Use Only

- *Work and Financial Management*: Verifying that activities align with time, quality, and cost standards outlined in the activity work plans for Pagkilos facilitators and beneficiary communities;
- *Adherence to Standards*: Monitoring compliance with the various Pagkilos technical sub-manuals;

Most M&E tools are designed for operations monitoring and are used by both M&E Officers and program staff at various levels. It is essential that all implementers are familiar with their roles in data collection, quality assessment, and analysis. Monitoring data is entered into the Management Information System (MIS). To support the monitoring process, monthly learning and information-sharing sessions with the management team, ACT, and MCT will be held. These sessions aim to provide timely technical assistance, promptly address red flags, and resolve issues that could impact the effective implementation of community resilience activities.

3. ***Capacity Building (CapBuild) Monitoring***

Monitoring of capacity building interventions are for the purposes of determining whether training conducted are relevant to project needs and effective in driving project outcomes.

The type and composition of training activities are designed to disseminate project plans and capacitate project personnel with the necessary skills and knowledge to implement project activities. These are to be cascaded by the NPMO to the RPMO and RPMO to the ACT, MCT and Community/Barangay levels.

Targeted training interventions may be implemented in identified areas based on their KPIs. Effectivity of training interventions are evaluated during the activity itself (pre- and post-test), as well as through the monitored changes in the performance of the targeted area for intervention.

4. ***Environmental and Social (E&S) Monitoring***

Environmental and Social (E&S) Monitoring under the Pagkilos ensures that environmental and social risk management measures are effectively

Official Use Only

implemented throughout the project lifecycle. The National Project Management Office (NPMO), supported by Regional Project Management Offices (RPMOs), Area Coordinating Teams (ACTs), and trained community volunteers, leads the regular monitoring and reporting of E&S performance. Monitoring activities are based on the Environmental and Social Commitment Plan (ESCP) and the Environmental and Social Management Framework (ESMF), with specific requirements detailed in Subproject Environmental and Social Management Plans (ESMPs). E&S Reporting consists of the following: a.) regular reporting; b/) incident reporting; d.) completion report of the project.[17]

E&S monitoring covers regular performance reporting, incident and accident reporting, and final evaluation through a completion report. Regular monitoring results are integrated into overall project progress reports submitted to the World Bank and relevant oversight agencies. In cases of serious incidents or accidents, the NPMO must notify the World Bank within 48 hours of learning of the event. The project completion report will assess the overall implementation of the ESMF and recommend further measures for continued environmental and social risk management during the transition to local government units (LGUs).

To facilitate structured E&S monitoring, an Environmental and Social Management System (ESMS) will be established as part of the project's Management Information System (MIS), serving as the official repository for E&S data and reporting processes. Details on the monitoring scope, frequency, and responsible entities are further elaborated in the Pagkilos Operations Manual and related Sub-Manuals.

5. ***Community Monitoring***

Community Monitoring (CM) consists of several activities that start with the Participatory Risk, Vulnerability, and Capacity Assessment (PRVA) for the Community Resilience Implementation Process (CRIP).

At the start of the CRIP, Community Volunteers (CVs) are assigned areas for

[17] Refer to the Section 6.4 of the SMF for the details on the types, scope, frequency and responsible entities for E&S reporting

Official Use Only

systematically gathering, verifying, and confirming key socio-economic and demographic information of the community through the Community Profile to be accomplished. The Community Profile comprises the following sections: i.) Physical Information; ii. Demographic; iii. Economics; iv. Social Welfare; v. Health and Nutrition; vi. Education; vii. Housing and Infrastructure; viii. Environmental and Econological; ix. Disaster Risks; and x. Governance and Community

The Community Profiling and Validation activity is further supplemented by the Barangay Risk and Vulnerability Mapping (BRVM) and the Focused Group Discussions (FGDs). The BRVM intends to produce a map providing a visual overview of risks across the barangay, and if applicable, to other adjacent barangays as well.

Following this, the FGD serves to deepen the understanding established in accomplishing the community profile and creation of the community risk map. As discussed in SM1, separate FGDs will be conducted for the following groups

Economic Groups	:	Participants with shared livelihood interests.
Indigenous Peoples	:	A separate FGD will be held for IPs if they are a minority in the barangay
Community para-professional and other interest groups	:	Barangay Health Workers (BHWs), Midwives, Teachers, Day Care Workers, Youth Representative, Representative for Persons with Disability
Women	:	Separate FGD with women could be convened or they can be represented in all the aforementioned groups

FGDs are moderated discussions facilitated by the ACT and CV, with another CV serving as the note-taker in each group. To encourage participants to share their ideas and insight, it is also recommended that circular seating arrangements be implemented to make it easier for participants to respond to each other. If the discussion is to be recorded, the facilitator should seek permission from the participants.

In documenting the discussion, it is important to actively listen for the

Official Use Only

following:

- Consensus and Dissensus: *Did everyone agree immediately or were there disagreements to what was raised?*
- Identify themes: *What are themes in which the discussions points can be grouped accordingly*
- Verbatim Quotes: *Some points raised may be best documented as quotes in the documentation.*

This process involves facilitating the active participation of community members to ensure the accuracy and completeness of data. This is crucial for the identification of vulnerabilities, identification of priorities, and later on the appropriate interventions needed.

What was found out in the preparation of the Community Profile, preparation of the Vulnerability Map, and conduct of the FGD will be presented during the Barangay Risk and Vulnerability Workshop. The objective of this activity is to build a common understanding of the major risks that will affect their barangay as well as the range of causes and effects of these risks.

Following the Municipal-wide PRVA and Resiliency Planning and before the Sub Project Development Workshop (SPDW), CVs will be organized into the Community Sub-Project Management Committee (CSPMC). The CSPMC will be responsible for the preparation of the proposal and, subsequently the implementation of sub projects; managing financial disbursement; preparation/submission of periodic reports as required by the project.

The Community Monitoring Sub-Committee (CMSC) is one of the committees under the CSPMC. This subcommittee is responsible for the monitoring of the approved plans to ensure compliance and track-barangay level progress against project KPIs and SP specific KPIs.

Insights generated through Community Monitoring are intended to inform the design of local activities that promote community development. Additionally, this information is valuable to the Pagkilos itself and is included in the Program's database system, serving as reference material for monitoring KPIs and informing future adjustments to program design and implementation. M&E Officers at the RPMO and NPMO levels are expected to

Official Use Only

periodically check the activation and effectiveness of the CM system in program areas, offering technical assistance as needed.

6. ***Oversight Monitoring***

Oversight Monitoring under the Philippine Community Resilience Project (Pagkilos) is conducted by national and regional oversight bodies to ensure compliance with program policies, uphold quality standards, and maintain alignment with strategic objectives. It involves cross-regional reviews, supervisory visits, spot checks, and validations of field reports and MIS data, providing independent verification of the fidelity of implementation, quality of services, resource utilization, and responsiveness of project activities.

Oversight monitoring identifies systemic issues, informs management decisions, and supports continuous program improvement. It also ensures that accurate and reliable information is regularly reported to the National Steering Committee (NSC) for PCRP, as well as to external oversight bodies such as the World Bank, National Economic and Development Authority (NEDA), Department of Budget and Management (DBM), and Commission on Audit (COA), promoting transparency, accountability, and evidence-based decision-making at all levels.

3.2. Evaluation

Evaluation is the systematic and objective assessment of an ongoing or completed project to determine its relevance, effectiveness, efficiency, sustainability, and impact.

Program implementation entails an ever growing need for evidence-based policy making and planning. This is to understand the local context and realities of communities being served, as well as the interplay of policies vis-a-vis poverty and vulnerability. Knowledge, therefore, is a key organizational resource, and knowledge production seeks out the surest path towards empowerment and lasting change.

3.2.1 Types and Purposes

Internal Evaluations are those initiated and implemented by KALAHI-CIDDS, and or by the Policy Development and Planning Bureau (PDPB). These are focused on

Official Use Only

providing assessments that identify needed steering measures during project implementation and provide data-driven recommendations to inform future expansions of the program. Given the time-sensitive nature of its contributions, these are conducted during project implementation and integrated into regular reports.

External Evaluation are those that necessitate an external implementer - whether an academic institution, development partner, independent researcher, Highly Technical Consultant (HTC). Some research areas and designs are more cost-effective when outsourced. These would be studies that necessitate larger sample sizes and require extensive data gathering or coordination with other government agencies - which may be difficult to conduct by project personnel with other functions pertaining to project implementation.

3.3. Research Agenda

Comprises six priority studies throughout the five-year implementation of the PCRP. These primary studies are to be conducted externally by consulting firms or consultants procured. Additional studies may be proposed (which may be conducted internally or externally) as needed and approved by the NPMO.

Table 7:Priority Studies by Year

Year	Study	Focus	Implementer
Year 1 - 2026	Baseline Study	Community Resilience / Institutional Support for Resilience	Consulting Firm
Year 2 - 2027	Special / Thematic Study	To be determined	Consultant
Year 3 - 2028	Midline Study	Community Resilience / Institutional Support for Resilience	Consulting Firm
	Special / Thematic Study	To be determined	Consultant
Year 4 - 2029	Special / Thematic Study	To be determined	Consultant
Year 5 - 2030	Endline Study	Project Development	Consulting Firm

Official Use Only

		Outcomes Community Resilience / Institutional Support for Resilience	

Periodic assessments, namely the baseline, midterm, and endline studies, evaluate the progress and achievements in relation to established goals and targets. These will focus on assessing the accomplishment of project development objectives through the in-depth evaluation and analysis of the progress being made in improving community resilience and building institutional support for it.

Baseline, midline, and endline studies, as their name implies, will assess project development outcomes before, during, and after project implementation. Specifically,

Establish baseline, midline, and endline values for Key Performance Indicators (KPIs) under Project Development Outcomes (PDOs). Having comprehensive and detailed pre-, during, and post- project measurements of PDOs can provide a reference or point of comparison to evaluate progress being made during project implementation

Assess current institutional capacities of Local Government Units (LGUs) in resilience planning and implementation. The study identified the most vulnerable municipalities in terms of poverty incidence in relation to climate risks, stunting, and IP population. From this, the study will provide a comprehensive assessment of these municipal LGUs to identify facilitating and hindering factors in creating and implementing policies for promoting resilience and reducing climate risk.

Identify existing vulnerabilities to natural hazards. It follows that these municipalities would also have communities among the most vulnerable to natural hazards. As such, the study will also seek to provide a comprehensive assessment of community vulnerabilities to natural hazards and how these may be exacerbated with other vulnerabilities pertaining to gender, indigeneity, disability, and age.

Official Use Only

Provide recommendations on project interventions and implementation strategies. The study will provide insight that may inform decisions and steering measures to be made by the NPMO, and/or for future KALAHI-CIDSS modalities, as well as the broader audience for CDD and social welfare in general (i.e. development partners, other NGAs).

Special / Thematic Studies have a specific focus and/or conducted during key points in the project cycle. Having a specific thematic focus, special studies may interrogate specific aspects of the PCRP, and/or results of a particular project policy, aspect or design.

The specific focus and design of these studies are to be determined during project implementation, subject to program needs, and strategic directions to be taken. These special/thematic studies may also be informed by the findings of periodic studies or by the various reports from the field offices. Insight from these studies will be used to inform future legislation and refine national policy directions.

3.3.1 Study Protocols and General Procedures

Proposals for evaluation studies are to be approved by the NPMO. This is to ensure its ethical design and conduct, and strategic alignment of the evaluation with the program's scope, learning agenda, policy development, and evidence-based decision-making. Studies to be conducted are to be implemented in accordance of the following department guidelines:

- DSWD Memorandum Circular No. 9 S. 2019. Guidelines for the Conduct of Research and Evaluation in the DSWD;
- DSWD Memorandum Circular No. 10 S. 2019. Protocol for the Conduct of the Research Studies in the DSWD Offices, Centers, and Institutions, including the Request of SWD Data/Information
- DSWD Memorandum dated 16 July 2024. "Establishment of the PDPB Research and Evaluation Advisory Group"
- DSWD Memorandum Circular No. 27 S. 2024. Protocol for the Conduct of Research Studies in DSWD Offices, Centers and Institutions Amending Memorandum Circular No. 10. S. 2019
- DSWD Research and Evaluation Agenda 2023-2028
- Other policies as applicable

Official Use Only

Given the project's contribution to national plans and international commitments, the Pagkilos' evaluation will also take into consideration the NEDA-DBM Joint Memorandum Circular (JMC) 2025-01 or the *'Revised National Evaluation Policy Framework of the Philippines'*. This is to ensure that the conduct of project evaluations would also serve to gauge the project's contributions to the Philippine Development Plan (PDP 2023-2028), National Adaptation Plan (NAP), Ambisyon Natin 2040, etc.

See Annex M for the Research and Evaluation Agenda.

3.4 Adherence to the Department's Data Privacy Policy

In adherence to RA 10173 or the Data Privacy Act of 2012, the department issued the Enhanced Data Privacy Manual in February 2026 which details the agency's policies and measure to prevent the unlawful collection, unauthorized access, accidental loss or destruction, misuse, unlawful alteration, and contamination of personal information.

M&E for the Pagkilos-PCRP will adhere to the policies and measures detailed in the Enhanced Data Privacy Manual. The following Data Privacy Principles will be observed throughout the project:

Transparency. The Department shall ensure that all data subjects understand the nature, extent of processing and the purpose of data processing. In addition, data subjects must be informed of the Department's data processing and its implications to their right to informational privacy. The data should be easy for the data subjects to access, update, and request deletion.

Legitimate Purpose. The Department must ensure that all personal data processing must have a legal basis or a legitimate purpose. The purpose/s must not be contrary to law, morals or public policy.

Proportionality. The Department shall only capture, store, process, and use necessary personal data based on what is needed to attain its program requirements or purpose. Data sharing must always be calibrated to stated legal purposes.

Official Use Only

Personal Information is defined as "*any information, whether recorded in a material form or not, from which the identity of an individual is apparent or can be reasonably and directly ascertained by the entity holding the information or when put together with other information would directly and certainly identify an individual*". Project monitoring, by necessity, will entail the routine collection of personal information through its project forms. To ensure the observance of RA 10173 and the Department's data privacy policies, the following protocols will be observed

A. Participants/Data Subjects will be informed of their rights and their voluntary participation in the activity and provision of information
B. Project Forms, such as attendance sheets, collecting personal information of multiple individuals will include a printed notice on how participants are providing their consent on the use and processing of their personal information by filling out the form.
C. Project Forms, such as the CV Profile Form, collecting detailed Personal Information of a single individual per form will be accomplished with an accompanying Data Consent Form (see Annex N)
D. During project activities, the facilitator shall inform the participants that data will be gathered for the purpose of documentation, and will be made aware of the voluntary nature of their participation and collection of data.

As detailed in General Data Privacy Principles of the Enhanced Data Privacy Manual, the project shall ensure that the participants/data subjects are aware of the nature, purpose, and extent of the processing of personal data. Through adhering to the abovementioned protocols, participants / data subjects are able to make an informed consent in providing their personal information and the following rights are upheld:

a. Right to be informed;
b. Right to object;
c. Right to access;
d. Right to rectification
e. Right to erasure or blocking; and
f. Right to damages.

Official Use Only

PART 4. M&E IMPLEMENTATION PROCESS

The Monitoring and Evaluation (M&E) implementation process for the *Philippine Community Resilience Project (Pagkilos)* is designed to ensure that project progress is systematically tracked, analyzed, and utilized to inform decision-making at all levels. The process follows a step-by-step approach, with each step aligned with the project's objectives and grounded in national and international standards.

4.1. Steps in Implementing M&E

Step 1: Understanding the Process, Protocols, and Standards

By design, the Pagkilos-PCRP follows a pre-defined *process* i.e. a set of related, structured, and sequential activities and deliverables intended to accomplish the project's development objectives - this is the Community Resilience Implementation Process (CRIP). Monitoring and Evaluation(M&E), being embedded throughout the program phase, serves to systematically track and measure the progress of activities and its intended deliverables as CRIP is being implemented. A more detailed and in-depth discussion of the CRIP and each activity can be found in the Social Mobilization Sub-Manual.

Protocols are in place to ensure the integrity of the CRIP - activities and their outputs are accomplished in the way they are intended without voiding their contribution to the PDO. These ensure that the implementation of the project remains aligned with its guiding principles. Specific protocols for each sector are detailed in the procurement, engineering, finance, capacity building, etc. sub-manuals.

In the context of M&E, protocols primarily concern the proper handling and processing of data - from collection, encoding, and reporting. Protocols are a structured system of checks and balances, and its observance decreases the likelihood of erroneous and questionable data from being captured in the system due to being screened through multiple levels of accountability. It may be helpful

Official Use Only

to reflect on the following questions to gauge whether proper protocols are being observed:

- Has it been accomplished by the rightful person/s?
- Has it been reviewed and approved by the rightful and authorized person/s?
- Has it been submitted/uploaded with a Means of Verification (MOV)?

Relatedly, certain standards need to be met for a form, report, etc. to be approved and submitted. When a form or report does not meet standards, such as when it is improperly filled out, lacks information, or untruthful, it is deemed unsatisfactory and unfit to be consolidated in higher level reports or be used for decision-making purposes.

Step 2: Data Collection

Data collection refers to the systematic and timely collection of information through proper project forms and methodologies. Forms can be understood as tools to gather qualitative and quantitative data. We can categorize project forms as a.) KPI Contributory Form; b.) Process Form; c.) Safeguards Form; d.) SP Form; and e.) Community Finance Forms.

KPI Contributory Forms are those that contain fields that are used to measure the accomplishment of Key Performance Indicators (KPIs). These forms are the most crucial to the project and often have set deadlines for encoding since KPIs are included in almost all regular/routine reports.

Process Forms are those accomplished as part of- or as a result of- an activity or a series of activities as part of the overall CRIP process or sub processes such as, for example, procurement activities, etc.. These serve to officially document the activity's conduct and gather data that will serve as the basis of plans to be created, or are the plan itself.

SP Forms, as the name suggests, are forms involved during project implementation. Some forms serve as pre-requisite documents to proceed with the next steps of the project. These also serve to document agreements and decision-mades as part of the community's management of project implementation. Additionally, having relevant project information documented in

Official Use Only

SP Forms ensures that the project is implemented in accordance to its original plan and/or serves as official documentation for any revisions or deviations made.

Safeguards Forms are accomplished to ensure compliance with social and environmental safeguards. Accomplishing these forms involves assessing whether the SP meets legal requirements as well as whether actual or potential harm and risks to the community or vulnerable groups are minimized.

Community Finance Forms record and, when approved, authorize the community's financial transactions. These forms are crucial to ensuring project funds are transparent and are utilized in the way they are intended.

Annex I provides an overview of the expected data to be gathered and collected by each accountability level.

Ensuring data quality is the responsibility of the individual or individual/s accomplishing the form as well as the authorized approver/signatory that would allow its submission to the next level of accountability. Data quality can be understood in terms of its six dimensions:

Table 8: Six Dimensions of Data Quality

Dimension	Description
Accuracy	Quality data measures what it is intended to measure i.e. closeness of agreement between the measurement and the true value of what is being measured[18]. This is also referred to as validity.
Reliability	data is reliable because they are measured and collected consistently. Data generated by the information system are based on protocols and procedures and do not change according to who is using them and when or how often they are used.
Completeness	means that an information system from which results are derived is appropriately inclusive.

[18] "International Vocabulary of Metrology – Basic and General Concepts and Associated Terms (VIM), 3rd Edition," International Organization of Legal Metrology, 2012, 50, https://doi.org/10.59161/JCGM200-2012.

Official Use Only

Precision	Quality data will reflect similar results when measured repeatedly under the same conditions. Precision refers to the closeness of agreement between indicators or measures obtained by replicate measurements[19]
Timeliness	Data are considered timely when they are up-to-date, and when information is available on time. Timeliness is affected by: (1) the rate at which the program's information system is updated; (2) the rate of change of actual program activities; and (3) when the information is actually used or required.
Integrity	Protected from deliberate or accidental biases.

Underpinning these dimensions is verifiability. Submitted forms and reports are to be reviewed and approved at each level - this protocol helps integrity of information being passed on to higher reporting levels. Additionally, it must be possible to validate and re-check the data when needed. As a guiding principle, Means-of-Verification (MOVs) are also to be submitted (uploaded in the MIS, submitted,etc.) and original copies to be kept on file in accordance with RA 9470[20].

Additionally, all project staff are duty bound to uphold the department's data privacy protocols as detailed in the Enhanced Data Privacy Manual[21]. For project forms that require the collection of personal information and personal sensitive information, it will be accomplished alongside the department's Declaration and Consent Form (see Annex N). For other forms that serve to document the conduct of activities, participants should be made aware of the voluntary nature of their participation and by participating in the activity they are consenting to be included in the documentation for the activity which may include but not limited to being included in the list of participants, included in photo documentation, have their responses and inputs to the activity be recorded/documented (e.g. captured through the barangay or municipal minutes form, etc.)

[19] "International Vocabulary of Metrology – Basic and General Concepts and Associated Terms (VIM), 3rd Edition," 52.
[20] Republic Act No. 9470, also known as "The National Archives of the Philippines Act of 2007," and its Implementing Rules and Regulations (IRR)
[21] FDSWD, "Enhaced Data Privacy Manual," Department of Social Welfare and Development, 2026.


Official Use Only

Step 3: Data Management

The KALAHI-CIDSS Information System (KCIS) serves as the centralized data management system intended to ensure that data is secured, protected, and accessible. The observance of rigorous protocols and well-defined standards in steps 1 and 2 are for the purpose of having quality and 'official' data reflected in the KCIS. Data reflected in official reports prepared by the NPMO and RPMO and submitted to stakeholders such as the World Bank, National Steering Committee (NSC), other National Government Agencies (NGAs), and other Development Partners, are to be sourced from the KCIS.

Data Flow refers to how data flows from one level of accountability to another, and is essentially transformed from existing as raw data in project forms accomplished at the community to becoming digital data encoded by the ACT/MCT, and aggregated into regional and national level tables. See figure below:

Figure 4: Data Flow from the Barangay to the National Level

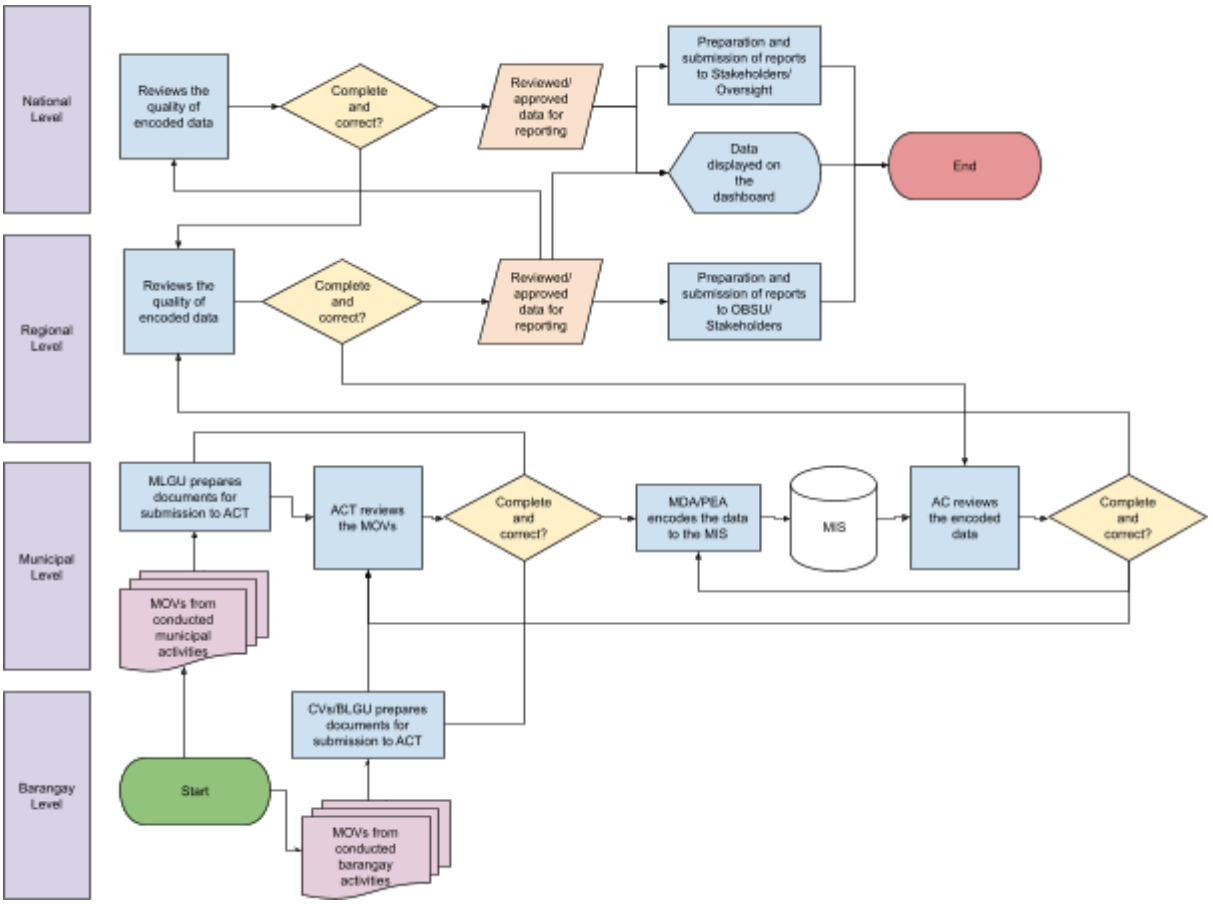

Official Use Only

Data security is the practice of protecting information from unauthorized access, corruption or theft throughout its entire life cycle. It encompasses every aspect of information security from physical security to administrative and access controls, and logistical security of software applications. The NPMO defines the system-wide permission for all accounts, and may delegate some system management permissions to the RPMO which include but are not limited to the creation and/or updating of user accounts, data amendments (to address errors), generation of reports, etc. within the scope of their region.

The Enhanced Data Privacy Manual defines a data breach as a "security violation in which unauthorized individuals or authorized individuals who unlawfully or negligently, access sensitive protected, or confidential data"[cite]. This may also include viewing, copying, transmitting, and in some extreme cases, stealing or using data without explicit permission.

Some examples of a data privacy breach are when personal data or the database containing personal data is: a.) accessed due to negligence; b.) processing for unlawful purpose; c.) accessed by unauthorized users; d.) used, disclosed, or disposed without authority; e.) updated or edited without authority; f.) lost or stolen; g.) transmitted to the wrong person; or h.) accessed, used, disclosed, disposed, updated, edited, lost, stolen, transmitted through identify theft [cite].

The scope of a privacy breach is not limited to the abovementioned examples. Should an incident of possible data privacy take place, the protocols detailed in the Enhanced Data Privacy Manual will be followed.

Periodic data audits and system generated reports help verify the consistency and integrity of data across levels. Should there be concerns with system data, these may be raised with the Regional M&E and may further be elevated to the NPMO when higher-level permissions are needed to address the concern.

Step 4: Data Analysis and Expected Outputs

Data analysis is deriving meaningful insights to inform decisions to be made. At the most basic level, data analysis during project implementation should answer whether *'will targets be accomplished on time?'*. Having quality, accurate, and

Official Use Only

frequently updated data better enables project managers - at any level - to identify possible challenges and shortcomings early on so measures can be taken to avert these.

When various data sets are taken together, they may reveal patterns as to where the delays are taking place or bottlenecks hindering progress and from there further interrogation and analyses can be made. The following guide questions may be helpful:

- Are the delays/non-accomplishment consistent with a specific community, municipality, or region?
- Are the delays/non-accomplishment consistent with a specific process or activity?
- Have the necessary inputs (human, financial resources) been provided in a sufficient and timely manner to accomplish the specific target?
- Do the same patterns appear in other project areas with the same or similar circumstances? Why or why not?

In some cases, answering these questions may necessitate consulting the volunteers and/or personnel responsible. Answers to these questions will guide and inform what is to be included in the narrative aspect of written reports. These will provide important context to why the accomplishment, KPI measurement, totals, etc. are as they are.


Step 5: Data Sharing and Utilization

In addition to project management and reporting, data is shared and utilized throughout all levels of the project - either as part of the CRIP activities or as reported with stakeholders. Data is presented publicly during activities such as but not limited to the *Municipal Orientation, Barangay Assemblies, MResT Technical Reviews, Operation and Maintenance Workshop, Functionality Audit, etc.* under the CRIP. Key Performance Indicators (KPIs) may be referred to and/or requested to be presented as 'program accomplishments' when they are presented in activities or events such as the State of Municipal Address (SOMA), PLGU's report during Regional Development Council (RDC) meetings, and various inter-agency meetings such as those of the KALAHI-CIDSS National Steering Committee (NSC) or any other inter-agency body (e.g. PDP Subcommittees) where the project is

Official Use Only

relevant or included in the agenda. See table below

Figure 5: Map of M&E Stakeholders by level and functional relationships

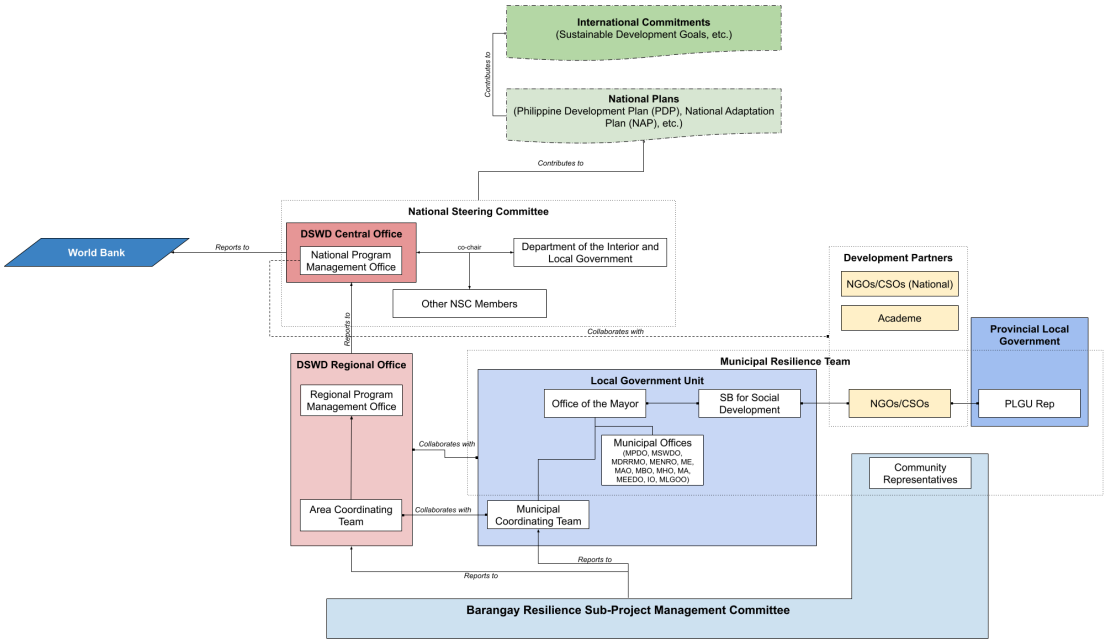

Given the Pagkilos-PCRP's multiple contributions to various national level goals, its accomplishments will also be included in national-level reports - likely aggregated with related interventions and/or greater emphasis on project impact i.e. accomplishments under outcome level indicators rather than intermediate indicators.

4.2. Organization and Management


4.2.1. Organization

Monitoring and Evaluation (M&E) functions and focals are lodged under the Policy Development and Compliance Division (PDCD). The PDCD spearheads the formulation and enhancement of key policy instruments such as manuals, guidelines, guide notes, etc. towards promoting efficient and effective program implementation. These policy instruments function in parallel with the division's built and maintained information systems for monitoring and tracking performance (such as in the MIS), ensuring accurate data collection, reporting, and compliance with environmental and social safeguards. It is headed by a Project Development Officer V (PDO V) and further divided into two sections: a.)

Official Use Only

System Development and Maintenance Section; and 2.) Policy Development and Data Management Section.

Figure 6: Structure of the NPMO Policy Development and Compliance Division

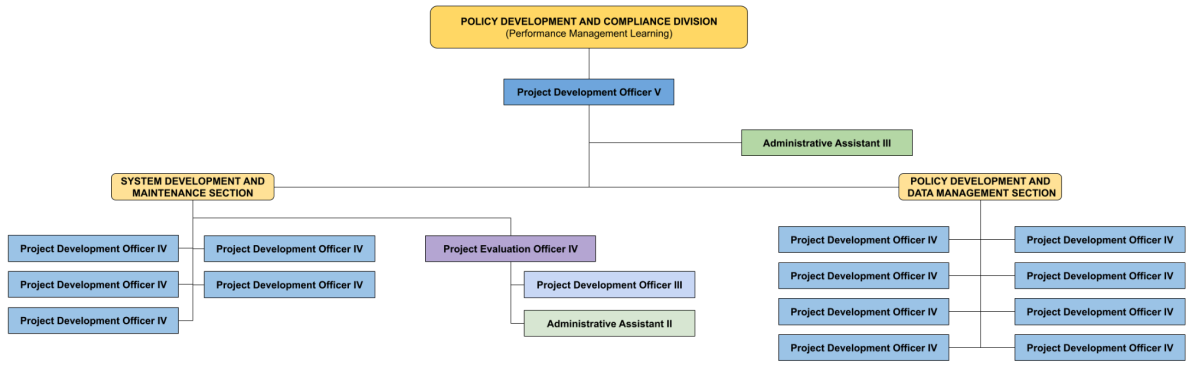


Dedicated focals for specific M&E functions are assigned in each section. Under the Policy Development and Data Management Section, there are focals for monitoring, evaluation/research, finance, community development, environment and social safeguard. On the other hand, the System Development and Maintenance Section has focals for front-end and back-end system development, database management, dashboard development.

At the RPMO level, the M&E Section is headed by a Project Evaluation Officer IV and leads a team consisting of Project Evaluation Officers III and III. The regional M&E section will focus on reporting and database functions, specifically: 1.) preparation of regular reports; 2.) ensuring accuracy, completeness, and timeliness for data encoding and reports to be consolidated at the regional level, 3.) analyzing project data for inclusion in reports; and other related tasks


Official Use Only

Figure 7: Structure of the RPMO Monitoring and Evaluation Section

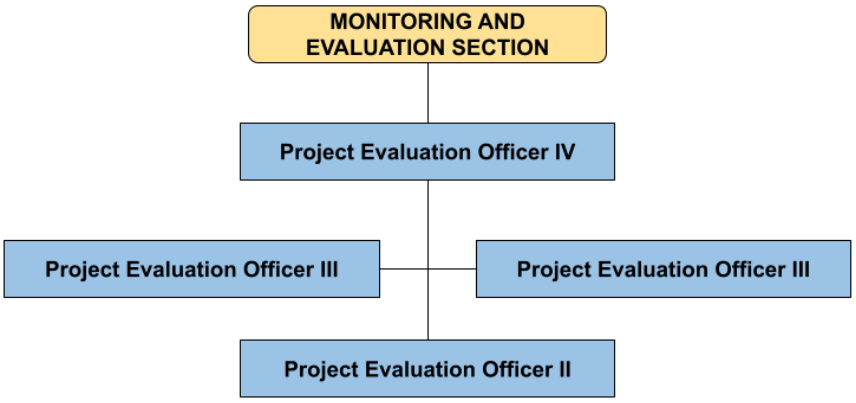

Both the reports and database teams are to work closely with the ACT and MCT to ensure their compliance with encoding and reporting deadlines - under the supervision of the PDO III and the NPMO.

Figure 8: Structure of the ACT and MCT



The Area Coordinator (AC) oversees project implementation in the communities to ensure alignment with the Pagkilos goals of building resilient communities. This role involves coordinating with the LGUs, barangays, and other stakeholders to ensure the success of program activities and support inclusive, participatory governance.

Similarly, the MAC has the same function of overseeing project implementation in the communities belonging to their respective municipalities. The AC and MAC work together to monitor the progress of sub projects, actively resolving issues encountered during implementation to achieve resilience building objectives. They also share in the responsibility of ensuring the CDD approach is followed and community-led development efforts are strengthened through effective coordination.

Community Facilitators (CEF), in both the ACT and MCT, are responsible for

Official Use Only

facilitating community mobilization and engagement activities, ensuring that local communities are informed, engaged, and actively participate in resilience-building efforts. This role promotes participatory governance and empowers community leaders to take ownership of resilience initiatives. They also provide capacity-building support to local community leaders, enhancing their ability to identify risks, prioritize projects, and implement sustainable community-driven development. Ultimately, the facilitator works to strengthen social capital within communities, fostering cooperation and collective action to address environmental hazards and vulnerabilities.

Technical Facilitators (TF), in both the ACT and MCT, provide crucial technical expertise and support for the implementation of community infrastructure and other program components. They conduct essential site visits and ensure quality assurance across all technical aspects, including adherence to engineering standards and principles of environmental sustainability, thereby aligning with the Philippine Community Resilience Program's (Pagkilos) resilience-focused objectives. A key aspect of their role involves close collaboration with local contractors and community members to guarantee the effective and long-term sustainability of subprojects. Furthermore, the TFs are responsible for ensuring that all subproject implementations meet stringent environmental safeguards to strengthen climate and disaster resilience within the communities.


Municipal Financial Analysts (MFA), in both the ACT and MCT, play a critical role in overseeing financial implementation within the area, ensuring that funds are utilized efficiently for resilience-focused subprojects. This position involves assisting in the meticulous preparation of financial reports for submission to both Regional Program Management Offices (RPMOs) and the National Program Management Office (NPMO).

Official Use Only


ANNEXES

Official Use Only

ANNEX A: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) THEORY OF CHANGE

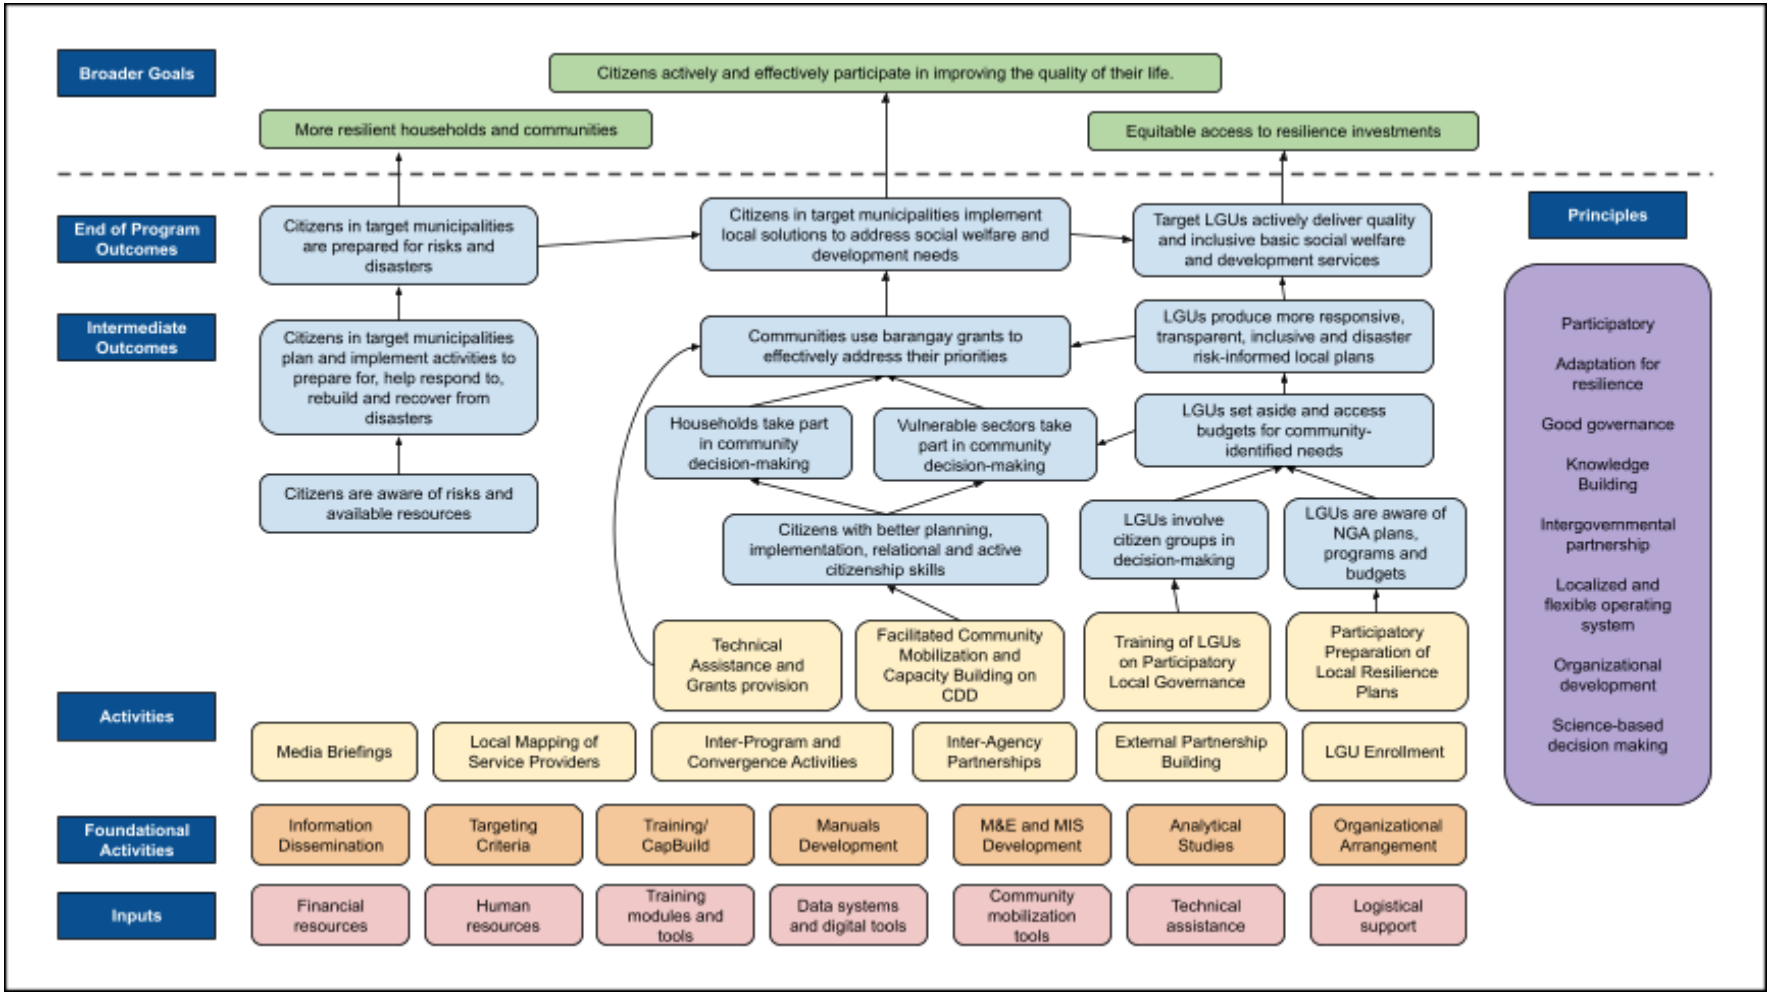


ANNEX B: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS CHAIN

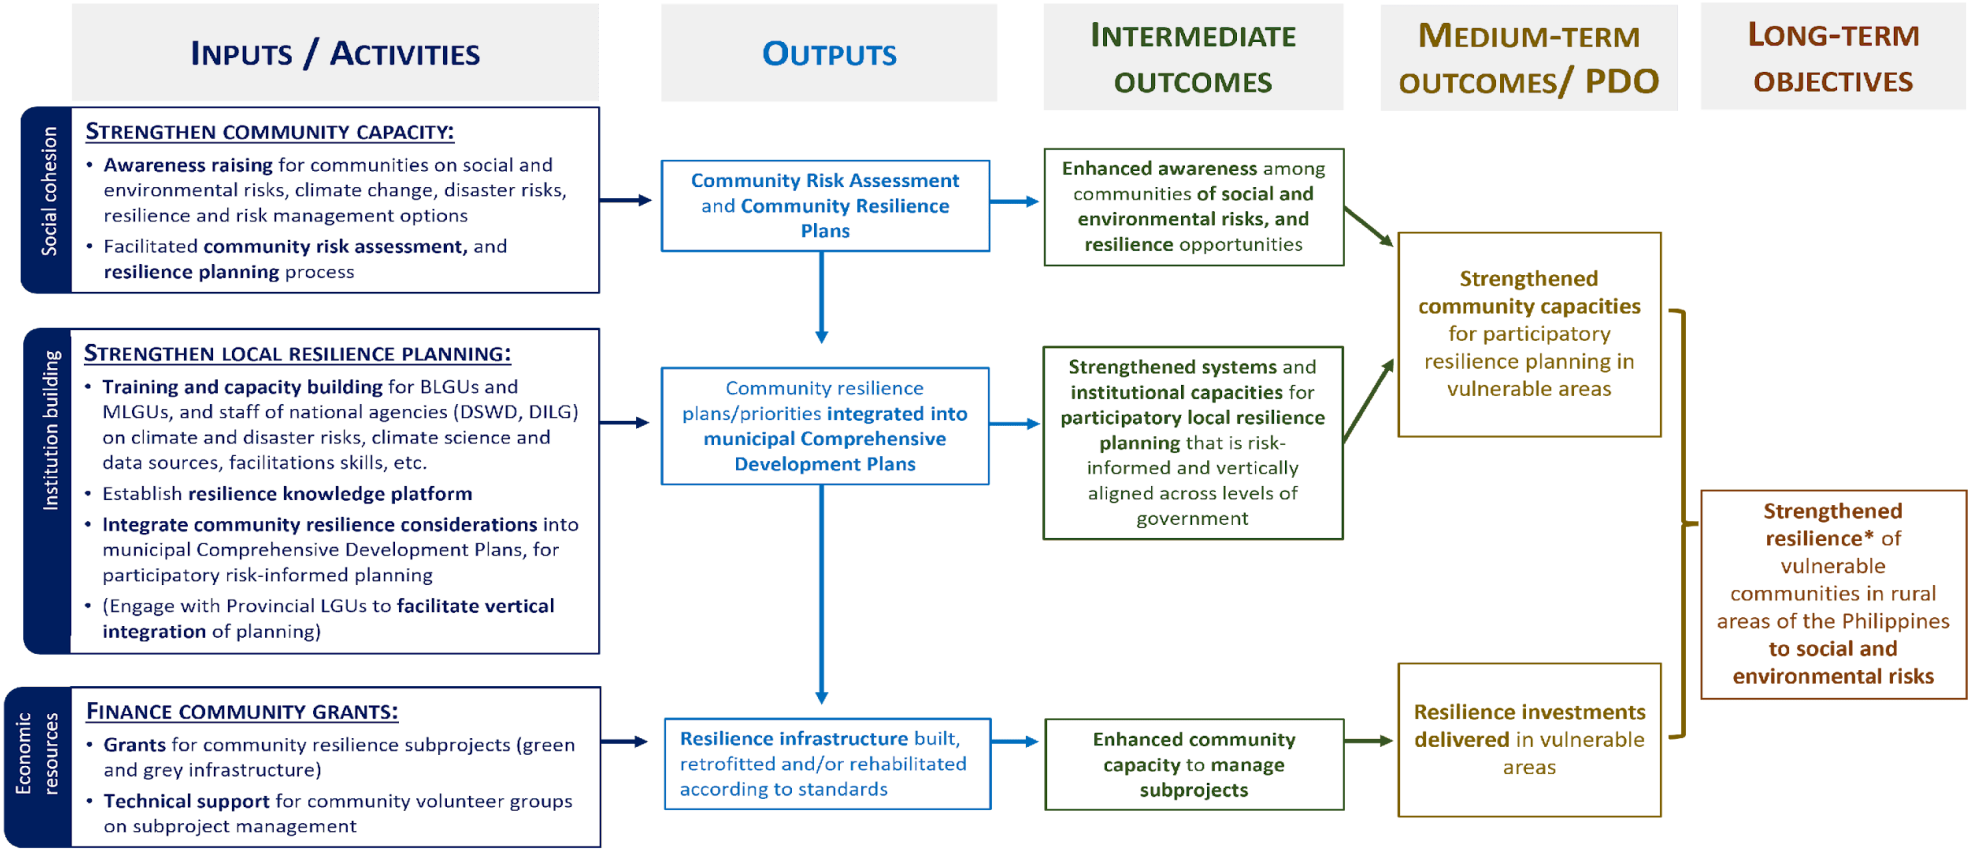

Note: Overall resilience at the municipal level will be achieved through the CDPs, which the Project is expected to influence through the community-led resilience plans, trainings, and support provided to the municipal local government units (MLGUs) and staff of national agencies. However, the totality of investment needs outlined in the CDPs will be beyond the scope of the project investments, which will finance only part of the CDP resilience activities.

Official Use Only

ANNEX C: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS FRAMEWORK[22]

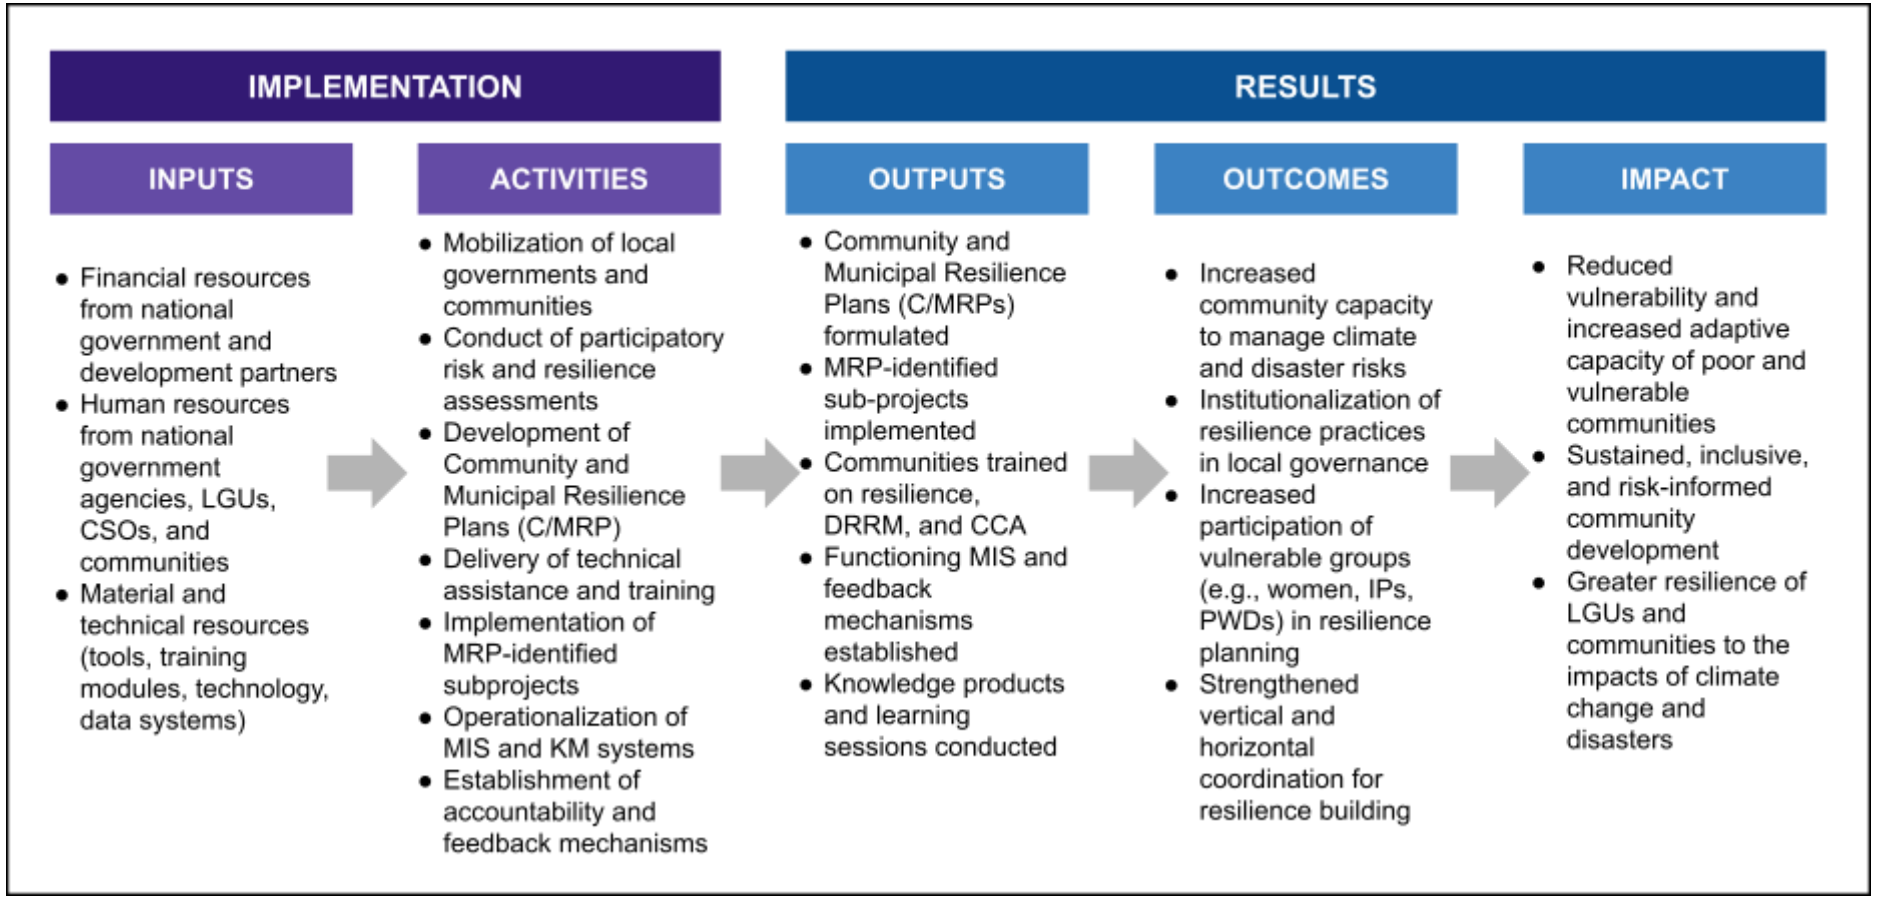

[22] Based on the NEDA-approved Pagkilos Results Framework and Logical Framework, in accordance with the CY 2024 Guidance Note on the Development of Program/Office Monitoring and Evaluation (M&E) Plan issued by the DSWD Policy Development and Planning Bureau (PDPB).

ANNEX D: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) RESULTS MATRIX[1]

	Indicators	Baseline	Target						End Target	Means of Verification	Assumptions / Risks
			2025	2026	2027	2028	2029	2030			
(a)	*(b)*	*(c)*	*(d)*						*(e)*	*(f)*	*(g)*
Impact: Resilience of communities and institutions increased											
Project Development Objective (PDO) Indicators by Objectives/ Outcomes											
PDO: Strengthen community capacities for participatory resilience planning and increase resilience investments in vulnerable areas	% of beneficiaries reporting that they can influence community resilience planning	0.00	-	-	-	-	-	70.00	70.00	Project Progress Report; Management Information System (MIS); Midterm and Endline Review Reports; CV Feedback Reports	Assumptions: (a) Compliance of Municipal Team to enhanced guidelines per Memorandum of Agreement; (b) timely delivery of local counterpart contribution and technical support; (c) openness of community members to risk and vulnerability assessment and resilience planning.
	% of municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP)	0.00	-	-	-	-	-	85.00	85.00	Finalized CDPs approved by Municipal Councils and endorsed to DILG; Municipal Council Resolutions	Risks: (a) Limited cooperation of LGU team; (b) Elite capture by influential officials; (c) Occurrence of disaster event
	% of the population in target areas benefitting from resilience investments *(cumulative)*	0.00	-	-	70.00	70.00	70.00	70.00	70.00	Project Progress Report; MIS; PSA Data; Municipal Profile; SPCR (supported by FA Report and Certificate of Completion and	

	Indicators	Baseline	Target						End Target	Means of Verification	Assumptions / Risks
			2025	2026	2027	2028	2029	2030			
(a)	*(b)*	*(c)*	*(d)*						*(e)*	*(f)*	*(g)*
										Acceptance (COCA))	
Intermediate Results Indicators by Components											
Component 1: Community Grants for Resilient Planning and Investment	% of communities trained on risk and vulnerability assessment and resilience planning	0.00	-	35.00	60.00	80.00	100.00	100.00	100.00	Project Progress Report; MIS; Training Documentation, including Attendance Logs	Assumption: a) Provision of adequate and appropriate technical and financial support by Pagkilos Inter-agency team; (b) Readiness of popularized and participatory tools/guides for enhancing risk and vulnerability assessment as well as resilience planning; (c) Full cooperation of local resilience Team
	% household participation in barangay assemblies for community resilience planning *(cumulative)*.	0.00	-	70.00	70.00	70.00	70.00	70.00	70.00	Project Progress Report; MIS; Activity Documentation including Attendance Logs	Risks: (a) Limited cooperation of LGU team; (b) Elite capture of influential staff/officials; (c) Occurrence of disaster event; (d) Misuse of funds
	% of communities with community resilience plans developed.	0.00	-	30.00	55.00	60.00	75.00	85.00	85.00	Project Progress Reports; MIS; Copies of Community Resilience Plans; Activity Documentation including Attendance Logs	
	% of investments in accordance with relevant national guidelines for resilience *(cumulative)*.	0.00	-	85.00	85.00	85.00	85.00	85.00	85.00	Project Progress Report; MIS; Sub-Project Proposals and Program of Works (POW); MResT resolutions signing-off/ recommending	

	Indicators	Baseline	Target						End Target	Means of Verification	Assumptions / Risks
			2025	2026	2027	2028	2029	2030			
(a)	*(b)*	*(c)*	*(d)*						*(e)*	*(f)*	*(g)*
										the proposals and technical design/ POW; Minutes of MResT meetings	
	% of municipalities with PLGU participation in the municipal- community resilience planning process.	0.00	-	30.00	35.00	40.00	40.00	40.00	40.00	Project Progress Report; MIS; Documentation of MResT/ MLGU/ community meetings, including Attendance Logs	Assumptions: (a) Provincial LGUs sign partnership agreement with DSWD
	% of sub-projects completed in accordance with approved technical plan and budget *(cumulative)*.	0.00	-	-	85.00	85.00	85.00	85.00	85.00	Project Progress Reports; MIS; SPCRs; FA Reports SP Procurement and Financial Reports	Risks: (a) Limited skilled workers in geographically isolated target areas; (b) Environmental and social risks are assessed to be substantial; (c) Resistance of community to adaptation
	% of sub-projects with sustainability ratings of satisfactory or better *(cumulative)*.	0.00	-	-	85.00	85.00	85.00	85.00	85.00	Project Progress Report; MIS; Sustainability Evaluation Reports	
	% of sub-projects with Operations and Maintenance (O&M) Plans with allocated annual budgets *(cumulative)*.	0.00	-	-	85.00	85.00	85.00	85.00	85.00	Project Progress Report; MIS; Sub-project Proposals and Plans, including O&M Plans; LGUs' (Barangay and/or Municipal) Annual Investment Plan (AIP) and Development Plan	
	% female participation in paid community labor *(cumulative)*.	0.00	-	-	35.00	35.00	35.00	35.00	35.00	Project Progress Report; MIS; SPCR; SP Procurement and Financial Reports, including Payroll	
	% of municipalities with at	0.00	-	30.00	60.00	70.00	80.00	90.00	90.00	Project Progress Report; MIS;	

	Indicators	Baseline	Target						End Target	Means of Verification	Assumptions / Risks
			2025	2026	2027	2028	2029	2030			
(a)	*(b)*	*(c)*	*(d)*						*(e)*	*(f)*	*(g)*
	least 40 percent women's representation in Municipal Resilience Teams (MResTs), with 30 percent (of the 40 percent) occupying or performing leadership roles.									MResT Resolutions and Meeting Documentation including Attendance Logs	
	% of women leaders in MResTs and Barangay Development Councils (BDCs) reporting meaningful involvement in decision-making processes *(cumulative)*.	0.00	-	90.00	90.00	90.00	90.00	90.00	90.00	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment)	
Component 2: Institutional Support for Local Resilience	% of municipalities with enhanced capacities on risk and vulnerability assessment and resilience planning.	0.00	-	40.00	65.00	75.00	90.00	100.00	100.00	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment); Municipal Resilience Plans developed	Assumptions: (a) Municipal staff participate in training; (b) Adequate funding and resources are provided; (c) Trainers are available and skilled Risks: (a) Low attendance due to competing priorities; (b) Logistical challenges in coordination
	Knowledge portal developed and installed.	No	-	Yes	Yes	Yes	Yes	Yes	Yes	Knowledge Portal, including Guidelines/ User Manual developed; Feedback from intended users Reports/ Data generated from the portal.	Assumptions: (a) Sufficient technical infrastructure; (b) Competent development team Risks: (a) Development delays or technical issues; (b) Data privacy and security risks.

	Indicators	Baseline	Target						End Target	Means of Verification	Assumptions / Risks
			2025	2026	2027	2028	2029	2030			
(a)	*(b)*	*(c)*	*(d)*						*(e)*	*(f)*	*(g)*
	% of municipalities with institutionalized Municipal Resilience Teams.	0.00	-	-	25.00	30.00	35.00	40.00	40.00	Project Progress Report; MIS; Municipal Council Resolution approving membership of MResT in the Local Development Council (LDC); LDC Meeting Documentation, including Attendance Logs.	Assumption: (a) Provision of adequate and appropriate technical and financial support by Pagkilos Inter-agency team; (b) Full cooperation of local resilience Team
	% of trained project staff at national and regional levels *(cumulative)*.	0.00		100.00	100.00	100.00	100.00	100.00	100.00	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment); Municipal Resilience Plans developed	Assumptions: (a) Relevant training materials and trainers available; (b) Staff can attend scheduled sessions.
Component 3: Project Monitoring and Management	% of grievances received that are addressed *(cumulative)*.	0.00	-	100.00	100.00	100.00	100.00	100.00	100.00	Documentation of Grievances; Referral reports to concerned units/ offices.	Assumptions: (a) Grievance mechanisms are accessible and trusted; (b) Adequate resources and staff are available for timely resolution Risks: (a) Low reporting due to lack of awareness or fear of retaliation; (b) Delays from limited capacity or poor coordination; (c) Incomplete or inaccurate grievance tracking

ANNEX E: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS)
INDICATOR TRACKING TABLE (ITT)

Level *(Regional / National)* : _____

Reporting Period : _____

Indicator	Baseline	Life of Project (LoP) Target	LoP Actual	% of LoP Target	Annual Target[2] [3]	Year to Date Actual	% of Annual Target	Q1 Reporting Period			Q2 Reporting Period			Q3 Reporting Period			Q4 Reporting Period		
								Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target
(a)	*(b)*	*(c)*	*(d)*	*(e)= (d)÷(c)*	*(f)*	*(g)*	*(h)= (g)÷(f)*	*(i)*	*(j)*	*(k)= (j)÷(i)*	*(l)*	*(m)*	*(n)= (m)÷(l)*	*(o)*	*(p)*	*(q)= (p)÷(o)*	*(r)*	*(s)*	*(t)= (s)÷(r)*
Project Development Objective (PDO) Indicators																			
% of beneficiaries reporting that they can influence community resilience planning	0.00	70.00																	
% of municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP)	0.00	85.00																	
% of the population in target areas benefitting from resilience investments	0.00	70.00																	

[23] Refer to column *(d)* of Annex D: Pagkilos Results Matrix for the Annual Target.

Indicator	Baseline	Life of Project (LoP) Target	LoP Actual	% of LoP Target	Annual Target[2] [3]	Year to Date Actual	% of Annual Target	Q1 Reporting Period			Q2 Reporting Period			Q3 Reporting Period			Q4 Reporting Period		
								Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target
(a)	*(b)*	*(c)*	*(d)*	*(e)= (d)÷(c)*	*(f)*	*(g)*	*(h)= (g)÷(f)*	*(i)*	*(j)*	*(k)= (j)÷(i)*	*(l)*	*(m)*	*(n)= (m)÷(l)*	*(o)*	*(p)*	*(q)= (p)÷(o)*	*(r)*	*(s)*	*(t)= (s)÷(r)*
(cumulative)																			
Intermediate Results Indicators																			
Component 1: Community Grants for Resilient Planning and Investment																			
% of communities trained on risk and vulnerability assessment and resilience planning	0.00	100.00																	
% household participation in barangay assemblies for community resilience planning *(cumulative)*.	0.00	70.00																	
% of communities with community resilience plans developed.	0.00	85.00																	
% of investments in accordance with relevant national guidelines for resilience *(cumulative)*.	0.00	85.00																	
% of municipalities with PLGU participation in the municipal- community	0.00	40.00																	

Indicator	Baseline	Life of Project (LoP) Target	LoP Actual	% of LoP Target	Annual Target[2] [3]	Year to Date Actual	% of Annual Target	Q1 Reporting Period			Q2 Reporting Period			Q3 Reporting Period			Q4 Reporting Period		
								Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target
(a)	*(b)*	*(c)*	*(d)*	*(e)= (d)÷(c)*	*(f)*	*(g)*	*(h)= (g)÷(f)*	*(i)*	*(j)*	*(k)= (j)÷(i)*	*(l)*	*(m)*	*(n)= (m)÷(l)*	*(o)*	*(p)*	*(q)= (p)÷(o)*	*(r)*	*(s)*	*(t)= (s)÷(r)*
resilience planning process.																			
% of sub-projects completed in accordance with approved technical plan and budget *(cumulative)*.	0.00	85.00																	
% of sub-projects with sustainability ratings of satisfactory or better.	0.00	85.00																	
% of sub-projects with Operations and Maintenance (O&M) Plans with allocated annual budgets.	0.00	85.00																	
% female participation in paid community labor *(cumulative)*.	0.00	35.00																	
% of municipalities with at least 40 percent women's representation in Municipal Resilience Teams (MResTs), with 30 percent (of the 40	0.00	90.00																	

Indicator	Baseline	Life of Project (LoP) Target	LoP Actual	% of LoP Target	Annual Target[2] [3]	Year to Date Actual	% of Annual Target	Q1 Reporting Period			Q2 Reporting Period			Q3 Reporting Period			Q4 Reporting Period		
								Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target
(a)	*(b)*	*(c)*	*(d)*	*(e)= (d)÷(c)*	*(f)*	*(g)*	*(h)= (g)÷(f)*	*(i)*	*(j)*	*(k)= (j)÷(i)*	*(l)*	*(m)*	*(n)= (m)÷(l)*	*(o)*	*(p)*	*(q)= (p)÷(o)*	*(r)*	*(s)*	*(t)= (s)÷(r)*
percent) occupying or performing leadership roles.																			
% of women leaders in MResTs and Barangay Development Councils (BDCs) reporting meaningful involvement in decision-making processes *(cumulative)*.	0.00	90.00																	
Component 2: Institutional Support for Local Resilience																			
% of municipalities with enhanced capacities on risk and vulnerability assessment and resilience planning.	0.00	100.00																	
Knowledge portal developed and installed.	No	Yes																	
% of municipalities with institutionalized Municipal Resilience Teams.	0.00	40.00																	
% of trained project staff at national and regional	0.00	100.00																	

Indicator	Baseline	Life of Project (LoP) Target	LoP Actual	% of LoP Target	Annual Target[2] [3]	Year to Date Actual	% of Annual Target	Q1 Reporting Period			Q2 Reporting Period			Q3 Reporting Period			Q4 Reporting Period		
								Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target	Target	Actual	% of Target
(a)	*(b)*	*(c)*	*(d)*	*(e)= (d)÷(c)*	*(f)*	*(g)*	*(h)= (g)÷(f)*	*(i)*	*(j)*	*(k)= (j)÷(i)*	*(l)*	*(m)*	*(n)= (m)÷(l)*	*(o)*	*(p)*	*(q)= (p)÷(o)*	*(r)*	*(s)*	*(t)= (s)÷(r)*
levels *(cumulative)*.																			
Component 3: Project Monitoring and Management																			
% of grievances received that are addressed *(cumulative)*.	0.00	100.00																	

ANNEX F: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) INDICATOR DOCUMENTATION SHEET[1]

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
PDO-Level Indicators																
Strengthen community capacities for participatory resilience planning and increase resilience investments in vulnerable areas.	% of beneficiaries reporting that they can influence community resilience planning	Beneficiaries reporting that they can influence community resilience planning	1 - sex 2 - gender 3 - age 4 - geographic location 6 - sector (Indigenous People (IP), Person with Disability (PWD)) Add'l: Poverty Level	% = (Actual / Target) x 100 **Actual:** Number of community representatives reporting that they have influenced the planning process. **Target:** Number of community representatives who participated in the planning activities conducted (community resilience planning, Municipal Resilience	Survey; Key Informant Interviews (KIIs)	Knowledge, Attitudes, Practices (KAP) Assessment; Community Volunteer (CV) Feedback Report	At midterm and end of the project	End of the project/ Impact Evaluation (IE); Implementation Completion and Results (ICR) Report	Project Progress Report; Management Information System (MIS); Midterm and Endline Review Reports; CV Feedback Reports	Regional Project Management Offices (RPMO); National Project Management Office (NPMO)	DSWD Management, National Economic Development Authority (NEDA), World Bank (WB), Local Government Units (LGUs)	0	N/A	1	1	0

[24] Included in General Appropriations Act (GAA)
[25] Aligned with Sustainable Development Goals (SDG)
[26] Aligned with Philippine Development Plan (PDP) 2023-2028
[27] Contributes to the Department of Social Welfare and Development (DSWD) Strategic Plan 2024-2028

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
				Teams (MResTs))												
	% of municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP).	Percentage of municipalities among the participating LGUs with completed community-led resilience plans integrated in the LGUs' CDPs; development of resilience plans followed a participatory approach providing venues for active participation of community members.	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of municipalities with community-led risk-informed CDPs **Target:** Total number of target municipalities	Review of records/ reports; Process documentation of community planning sessions	Finalized CDPs approved by Municipal Councils and endorsed to Department of the Interior and Local Government (DILG); Municipal Council Resolutions	At the end of the project	End of the project/ IE; ICR Report	Finalized CDPs approved by Municipal Councils and endorsed to DILG; Municipal Council Resolutions	MResTs; Area Coordinating Teams (ACTs); RPMOs; NPMO	DSWD Management, DILG, Department of Budget and Management (DBM), NEDA, World Bank, LGUs	0	DILG	1	1	1
	% of the population in target areas benefitting from resilience investments.	Percentage of population expected to benefit from the completed resilience investments; population is counted as the number of households (HHs) in communities covered by completed sub-projects (SPs) multiplied by a constant HH size.	4 - geographic location 6 - sector (IP, PWD)	% = (Actual / Target) x 100 **Actual:** Number of population (HH x HH size) residing in areas covered and/or serviced by the completed resilience investments. **Target:** Total number of population (HH x HH size) in covered barangays/ communities with resilience investments	Review of record/reports; Community validation activities	PSA Data; Municipal Profile; Sub-Project Completion Reports (SPCRs); SP Functionality Audit Reports (FAs)	Data should be collected and encoded into the MIS within 30 days after the completion of the sub-project.	Monthly: • GAA Physical Accomplishment Report • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report • GAD Report	Project Progress Report; MIS; PSA Data; Municipal Profile; SPCR (supported by FA Report and Certificate of Completion and Acceptance (COCA))	MResTs; ACTs; RPMOs; NPMO	DSWD Management, DBM, NEDA, World Bank, National Steering Committee (NSC), LGUs	1	4Ps	1	1	1

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
				implemented.				Semestral: • HPMES 5 Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR								
Intermediate Indicators																
Component 1: Community Grants for Resilient Planning and Investment	% of communities trained on risk and vulnerability assessment and resilience planning.	Percentage of barangays/ communities in participating municipalities with officials, staff, and community volunteers trained on risk and vulnerability assessment and resilience planning process.	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of barangays/ communities with pax trained **Target:** Total number of barangays/ communities in the target municipalities **annual targets based on phasing of municipal*	Desk review; Validation with training facilitators and focals from the LGUs	Project Progress Report; MIS; Training Documentation including Attendance Logs	Once, upon completion of training	Monthly: • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report Semestral: • HPMES 5 Annual:	Project Progress Report; MIS; Training Documentation including Attendance Logs	MResTs; ACTs; RPMOs	DSWD Management, DBM, NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
				project implementation				• ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR								
	% household participation in barangay assemblies for community resilience planning.	Percentage of HHs in the covered barangays/ communities represented in barangay assemblies for community resilience assessment/ planning/ validation activities.	1 - sex 4 - geographic location 6 - sector (IP, PWD)	% = (Actual / Target) x 100 **Actual:** Number of HHs represented during barangay assemblies **Target:** Total number of HHs in the target municipalities **annual targets based on phasing of municipal project implementation and anticipated and doable number of barangay assemblies per calendar year*	Desk review; Validation with relevant barangay officials and staff and community volunteers	Project Progress Report; MIS; Activity Documentation including Attendance Logs	Data should be collected and encoded into the MIS within seven days after the conclusion of each activity.	Monthly: • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report • GAD Report Semestral: • HPMES 5 Annual: • ODA Annual Portfolio Review • KALAHI-	Project Progress Report; MIS; Activity Documentation including Attendance Logs	MResTs; ACTs; RPMOs	DSWD Management, NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
								CIDSS Annual Report At the end of the project: • IE • ICR								
	% of communities with community resilience plans developed.	Percentage of communities among the participating Local Government Units (LGUs) with completed community-led resilience plans	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of barangays with community-led resilience plans **Target:** Total number of barangays in target municipalities	Review of records/ reports; Process documentation of community planning sessions	Project Progress Reports; MIS; Copies of Community Resilience Plans; Activity Documentation including Attendance Logs	Once, upon completion and availability of Community Resilience Plan	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Project Progress Reports; MIS; Copies of Community Resilience Plans; Activity Documentation including Attendance Logs	MResTs; ACTs; RPMOs	DSWD Management, DBM, NEDA, World Bank, LGUs	1	DILG	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
	% of investments in accordance with relevant national guidelines for resilience.	Percentage of community resilience investments planned and designed following the sector/ design-specific national standards and guidelines.	4 - geographic location Add'l: Sub-Project Type	% = (Actual / Target) x 100 **Actual:** Number of community investments with approved program of works/ sub-project designs verified to be compliant with relevant national standards and guidelines. **Target:** Total number of approved community investments in target municipalities **annual targets based on phasing of municipal project implementation*	Technical review and meeting of the MResTs Validation/Technical session with the community volunteer groups	Project progress reports Sub-project proposals and program of works MResT Resolutions signing-off/recommending the proposals and technical design/program of works Minutes of MResT Meetings	Once, upon completion and approval of the community resilience investment.	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Project Progress Report; MIS; Sub-Project Proposals and Program of Works (POW); MResT resolutions signing-off/ recommending the proposals and technical design/ POW; Minutes of MResT meetings	MResTs; ACTs; RPMOs	DSWD Management, NEDA, World Bank, NSC, LGUs	0	N/A	1	1	0
	% of municipalities with PLGU participation in the municipal-community resilience planning process.	Percentage of participating municipalities whose MResT meetings/ municipal-wide resilience planning session/s were attended by relevant representatives from the Provincial Local	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of municipalities with MResT Meeting/s attended by a PLGU representative	Review of meeting documentation	Project Progress Report; MIS; Documentation of MResT/ MLGU/ community meetings, including Attendance	Data should be collected and encoded into the MIS within seven days after	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report	Project Progress Report; MIS; Documentation of MResT/ MLGU/ community meetings, including	ACTs; RPMOs	DSWD Management,NEDA, World Bank, LGUs	0	N/A	0	0	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
		Government Unit (PLGU). PLGU representatives are able to provide technical assistance during the conduct of municipal-wide resilience planning session/s.		**Target:** Total number of target municipalities ** annual target based on phasing of municipal project implementation.*		Logs	the conclusion of each activity.	Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Attendance Logs							
	% of sub-projects completed in accordance with approved technical plan and budget.	Percentage of sub-projects designed, implemented, and completed in accordance with the approved technical plans and budget.	4 - geographic location Add'l: Sub-Project Type	% = (Actual / Target) x 100 **Actual:** Number of completed sub-projects in accordance with the approved technical plans and budget. **Target:** Total number of completed sub-projects ** annual target based on phasing of municipal project implementation and anticipated implementation period of community*	Validation sessions or meetings with MResT, community volunteers, and RPMOs	Project Progress Reports; MIS; SPCRs; FA Reports SP Procurement and Financial Reports	Data should be collected and encoded into the MIS within 30 days after the completion of the sub-project.	Monthly: • GAA Physical Accomplishment Report • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report • Publicized Government Projects/ Programs/	Project Progress Reports; MIS; SPCRs; FA Reports SP Procurement and Financial Reports	ACTs; RPMOs; NPMO	DSWD Management, DBM, Climate Change Commission (CCC), NEDA, World Bank, COA, NSC, LGUs	1	N/A	1	1	1

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
				sub-projects.				Activities (GPPA) Report Semestral: • HPMES 5 Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report • Commission on Audit (COA) Report • Climate Change Expenditure Tagging (CCET) At the end of the project: • IE • ICR									

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
	% of sub-projects with sustainability ratings of satisfactory or better.	Percentage of completed sub-projects evaluated as satisfactory or higher when sustainability evaluation guidelines and tools are applied.	4 - geographic location Add'l: Sub-Project Type; Sustainability Evaluation Rating	% = (Actual / Target) x 100 **Actual:** Number of completed sub-projects rated as satisfactory or higher. **Target:** Total number of completed sub-projects eligible for sustainability evaluation.	Site visits; Focus Group Discussions (FGDs)	Project Progress Report; MIS; Sustainability Evaluation Reports	Data should be collected, encoded and uploaded into the MIS within 7 days after the conduct of Sustainability Evaluation	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Project Progress Report; MIS; Sustainability Evaluation Reports	MResTs; ACTs; RPMOs	DSWD Management,, NEDA, World Bank, LGUs	0	N/A	1	1	0
	% of sub-projects with Operations and Maintenance (O&M) Plans with allocated annual budgets.	Percentage of sub-projects with prepared O&M plans allocated with budget by the LGU. O&M plans prepared at the sub-project planning stage.	4 - geographic location Add'l: Sub-Project Type	% = (Actual / Target) x 100 **Actual:** Number of SPs with O&M plans prepared at the start of the project and allocated with budget in the LGUs' development	Review of plans and proposals Validation sessions Municipal Budget Office and Municipal	Project Progress Report; MIS; Sub-project Proposals and Plans, including O&M Plans; LGUs' (Barangay and/or	Once, upon completion and availability of O&M plan.	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report	Project Progress Report; MIS; Sub-project Proposals and Plans, including O&M Plans; LGUs'	ACTs; RPMOs	DSWD Management, NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
		Budget for O&M plans/ activities included in the approved Barangay Development Plan (BDP) and/or Annual Investment Plan (AIP), as applicable based on the timing of the SP planning.		plan (AIP/BDP/CDP)* **Target:** Total number of sub-projects **may not be within the same budget year, as SP planning may not align with the timing of B/MLGU budget cycle.*	Planning and Development Office	Municipal) Annual Investment Plan (AIP) and Development Plan		Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	(Barangay and/or Municipal) Annual Investment Plan (AIP) and Development Plan							
	% female participation in paid community labor.	Percentage of community labor participants who are female in community resilience investments.	1 - sex 3 - age 4 - geographic location 6 - sector (IP, PWD)	% = (Actual / Target) x 100 **Actual:** Number of community labor participants who are female **Target:** Total number of community labor participants **annual target based on annual target based on phasing of municipal project implementation and anticipated implementation period*	Review of reports; Validation session with barangay LGU officials/ staff and community volunteers.	Project Progress Report; MIS; SPCR; SP Procurement and Financial Reports, including Payroll	Data should be collected, encoded and uploaded into the MIS as soon as ERS data is validated by ACT	Monthly: • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report • GAD Report Semestral: • HPMES 5 Annual: • ODA Annual Portfolio	Project Progress Report; MIS; SPCR; SP Procurement and Financial Reports, including Payroll	ACTs; RPMOs	DSWD Management, DBM, NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
				of community sub-projects.				Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR								
	% of municipalities with at least 40 percent women's representation in Municipal Resilience Teams (MResTs), with 30 percent (of the 40 percent) occupying or performing leadership roles.	Percentage of municipalities whose organized Municipal Resilience Team has at least 40% female membership. 30% of women members of the MResTs are identified as leaders. "Leader" is defined as those with key decision-making, management, and/or facilitative functions in the LGU Units/Divisions, organizations, or communities. The following will count as part of the 30% female members with leadership	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of municipalities with at least 40% female membership in MResT of which at least 30% are considered as leaders. **Target:** Total number of municipalities with organized MResTs	Review of reports Validation session with MResT secretariat	Project Progress Report; MIS; MResT Resolutions and Meeting Documentation including Attendance Logs	Data should be collected, encoded and uploaded into the MIS once the MOVs are available and can be updated before the program ends	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report • GAD Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE	Project Progress Report; MIS; MResT Resolutions and Meeting Documentation including Attendance Logs	ACTs; RPMOs	DSWD Management,NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
		roles – • Municipal Mayor, Vice Mayor, Sangguniang Bayan members (elected Municipal Councilors) • Division Chiefs of the LGU; Chairs and Vice-Chairs of LGU Special Bodies i.e. Local School Board, Local Health Board, etc • Barangay elected official (Brgy Captain and Councilors), core staff (Brgy Secretary, Brgy Treasurer) and Chairs of special Barangay LGU committees, i.e. Barangay Council for the Protection of Children, BDRMMC, Barangay Peace-Keeping Committee, etc. • Officers of CSOs • Community volunteers who are Chairs, Vice-Chairs,						• ICR								

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
		Coordinators of Community Sub-Project Management Committees (the committees managing the sub-projects)														
	% of women leaders in MResTs and Barangay Development Councils (BDCs) reporting meaningful involvement in decision-making processes.	Percentage of women leaders, BDC members, and/or MResT members, expressing increased or significant roles and/or contributions in the groups'/ Councils' decision-making process.	1 - sex 3 - age 4 - geographic location 6 - sector (IP, PWD)	% = (Actual / Target) x 100 **Actual:** Number of women leaders reporting meaningful involvement in decision-making process in covered municipalities of the project **Target:** Total number of women leaders involved in MResT and BDCs in covered municipalities of the project	Surveys with women leaders participating in the Project; KIIs; and FGDs with relevant informants	Case stories on women leaders of the project; Learning assessment, specifically learning application	Data should be collected, encoded and uploaded into the MIS once the MOVs are available and can be updated before the program ends	Monthly: • KPI Status Report • ODA Report Quarterly: • HPMES 4 • NEDA Alert Mechanism • WB Report • GAD Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment)	ACTs; RPMOs	DSWD Management,NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA**[24] *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG**[25] *(1-Yes; 0-No)*	**PDP**[26] *(1-Yes; 0-No)*	**DSWD Strategic Plan**[27] *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
								• ICR								
Component 2: Institutional Support for Local Resilience	% of municipalities with enhanced capacities on risk and vulnerability assessment and resilience planning.	Percentage of municipalities whose relevant officials, staff, and community volunteers with increased knowledge, attitudes, and skills on risk and vulnerability assessment and resilience planning, based post-training assessment (Pre-/Post-Test and Learning Application Assessment)	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of municipalities with 70% of trained pax (officials, staff, and community volunteers) registered increased scores in capacity assessment on risk and vulnerability assessment and resilience planning **Target:** Total number of municipalities with trained pax (officials, staff, community volunteers) on risk and vulnerability assessment and resilience planning	Observations	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment); Municipal Resilience Plans developed	Data should be collected, encoded and uploaded into the MIS once results of Post-Training and Learning Application Assessment are available	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Project Progress Report; MIS; Post-Training Assessment (Pre-/Post-Test and Learning Application Assessment); Municipal Resilience Plans developed	MResTs; ACTs; RPMOs	DSWD Management, NEDA, World Bank, LGUs	0	N/A	1	1	0
	Knowledge portal developed and installed.	Knowledge portal developed and installed; targets users able to utilize the portal as intended.	N/A	Availability of the Knowledge Portal for utilization of target users	KIIs; Survey with users	Knowledge Portal, including guidelines/ user manual developed	Quarterly	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism	Knowledge Portal, including Guidelines/ User Manual developed; Feedback from	RPMOs; NPMO	DSWD Management, NEDA, World Bank, LGUs	0	N/A	1	1	0

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
								• WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	intended users Reports/ Data generated from the portal.							
	% of municipalities with institutionalized Municipal Resilience Teams.	Percentage of municipalities whose project-organized MResTs transitioned to regular members of the LDCs.	4 - geographic location	% = (Actual / Target) x 100 **Actual:** Number of MResTs who become member of the LDCs **Target:** Total number of MResTs organized or target number of municipalities **Assumption:* *1 municipality = 1 MResT assessment and resilience planning*	Review of reports	Project Progress Report; MIS; Municipal Council Resolution approving membership of MResT in the Local Development Council (LDC); LDC Meeting Documentation, including Attendance Logs.	Data should be collected, encoded and uploaded into the MIS once the MOVs are available and can be updated before the program ends	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report	Project Progress Report; MIS; Municipal Council Resolution approving membership of MResT in the Local Development Council (LDC); LDC Meeting Documentation, including Attendance	RPMOs; NPMO	DSWD Management, NEDA, World Bank, LGUs	0	N/A	1	1	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
								At the end of the project: • IE • ICR	Logs.							
	% of trained project staff at national and regional levels.	Percentage of NPMO and RPMO project staff who received i) basic orientation on Pagkilos (objectives and targets, implementation process and components, and M&E and reporting) and ii) role-specific topic (social process, infrastructure, ESF, procurement, capbuild)	1 - sex 2 - gender 3 - age 4 - geographic location 6 - sector (IP, PWD)	% = (Actual / Target) x 100 **Actual:** Number of staff trained upon on-boarding **Target:** Total number of staff hired	Review of reports	Project Progress Report; MIS; Training Reports, including Attendance Logs.	Data should be collected, encoded and uploaded into the MIS once the MOVs are available and can be updated before the program ends	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Project Progress Report; MIS; Training Reports, including Attendance Logs.	RPMOs; NPMO	DSWD Management, NEDA, World Bank	0	N/A	0	0	0

Official Use Only

INDICATOR DOCUMENTATION											INVENTORY OF USERS AND CONTRIBUTION TO COMMITMENTS					
	Indicators	**Definition of Indicators**	**Disaggregation** *1 - sex* *2- gender* *3 - age* *4 - geographic location* *5 - income* *6 - sector*	**Computation**	**Data Collection Method**	**Data Source**	**Frequency of Data Collection**	**Frequency of Reporting/ Type of Report**	**Means of Verification**	**Responsible Unit**	**Users of the Information**	**GAA[24]** *(1-Yes; 0-No)*	**Cross-cutting Program / Oversight Office/ Other Actors**	**SDG[25]** *(1-Yes; 0-No)*	**PDP[26]** *(1-Yes; 0-No)*	**DSWD Strategic Plan[27]** *(1-Yes; 0-No)*
(a)	*(b)*	*(c)*	*(d)*	*(e)*	*(f)*	*(g)*	*(h)*	*(i)*	*(j)*	*(k)*	*(l)*	*(m)*	*(n)*	*(o)*	*(p)*	*(q)*
Component 3: Project Monitoring and Management	% of grievances received that are addressed.	Any type/ classification of grievances logged in the Project's records.	4 - geographic location Add'l: Type of Grievance	% = (Actual / Target) x 100 **Actual:** Number of grievances received, logged into the system, responded to, and addressed in accordance with the Project guidelines. **Target:** Total number of grievances received and logged into the system.	Review of reports; Validation with relevant unit/ office/ persons	Documentation of Grievances; Referral reports to concerned units/ offices.	Upon Conduct	Monthly: • KPI Status Report • ODA Report Quarterly: • NEDA Alert Mechanism • WB Report Annual: • ODA Annual Portfolio Review • KALAHI-CIDSS Annual Report At the end of the project: • IE • ICR	Documentation of Grievances; Referral reports to concerned units/ offices.	RPMOs; NPMO	DSWD Management, NEDA, World Bank, LGUs	0	N/A	0	0	0

Official Use Only

ANNEX G: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) CONTRIBUTIONS TO PHILIPPINE DEVELOPMENT PLAN (PDP) AND SOCIAL PROTECTION PLAN (SPP) 2023–2028

PDP Outcome / Sector Outcome	**SPP Goal / Objective / Outcome**	**Pagkilos Indicator**	**8-Point Socio-Economic Agenda Linkage**	**Relevant SDG Target(s)**	**Actual Accomplishment** *(What to Report)*	**Variance / Gap**	**Remarks / Notes / Data Source**
Enhanced Social Protection for the Vulnerable[28]	Expanded access to social protection and livelihood support[29]	% of target communities implementing resilience sub-projects	4. Strengthen social protection	SDG 1.3 – Social protection systems; SDG 11.5 – Reduce disaster impact	Number and percentage of target communities that have completed, and operationalized risk-informed sub-projects through participatory community processes.	Difference between planned and actual coverage / implementation	Data from MIS, community implementation reports, validation tools.

[28] Outlined in Chapter 3: Reduce Vulnerabilities and Protect Purchasing Power
[29] Aligns with the Strategic Focus Area A: Full Implementation of the Social Protection Floor

Improved Adaptive Capacities of Communities and LGUs[30]	Strengthened community-based mechanisms for risk reduction and response[31]	# of communities that completed risk-informed development plans	6. Climate-resilient communities	SDG 11.b – DRR in local planning; SDG 13.1 – Resilience to climate hazards	Report the number of barangays with completed and endorsed resilience plans, including elements like hazard assessment, DRRM, and social protection integration.	Gaps in completion rate vs. targets	Planning workshop documentation, approved community plans, and technical facilitation logs.
Empowered and Participatory Local Governance[32]	Strengthened participation of marginalized groups in social protection[33]	% of community members participating in decision-making (disaggregated)	5. Empowering communities	SDG 5.5 – Women's participation; SDG 16.7 – Inclusive decision-making	Provide participation rates from assemblies or planning sessions; disaggregate by gender, IPs,	Underrepresentation of certain sectors (e.g., IPs, women)	Field logs, community consultation forms, GESI scorecards.

[30] Discussed in Chapter 15: Accelerate Climate Action and Strengthen Disaster Resilience
[31] Corresponds to Strategic Focus Area B: Development of Adaptive and Shock Responsive Social Protection Programs
[32] Emphasized in Chapter 5: Modernize Agriculture and Agribusiness, focusing on community participation and empowerment.
[33] Part of the overarching goals in the SPP 2023–2028.

					PWDs, youth, etc.; describe methods used to ensure inclusion.		
Resilient Local Systems and Infrastructure[34]	Adaptive and shock-responsive social protection in LGU/community plans[35]	# of LGUs adopting Pagkilos planning and implementation standards	6. Disaster preparedness and infrastructure	SDG 11.b – DRR in local plans; SDG 9.1 – Resilient infrastructure	Indicate the LGUs that formally adopted PCRP-supported practices, planning tools, or technical standards in their local development and DRRM frameworks.	Targets not met due to policy or leadership constraints	LGU adoption documents, ordinances, minutes of technical working groups.

[34] Detailed in Chapter 15: Accelerate Climate Action and Strengthen Disaster Resilience.
[35] Aligns with Strategic Focus Area B in the SPP 2023–2028.

Strengthened Disaster Risk Reduction and Response[36]	Strengthened capacity of LGUs and communities for risk-informed program management[37]	# of LGUs trained; % of capacity improvement based on assessments	6. DRRM capacity building	SDG 13.1 – Climate adaptation; SDG 11.b – DRR in development	Number of trainings conducted, LGU attendance, pre/post capacity scores, documented changes in planning or coordination post-training.	Delays or gaps in training coverage	Training reports, evaluation forms, LGU self-assessment tools.
Data-Driven, Integrated Social Protection Systems[38]	Developed and integrated MIS for risk and vulnerability data[39]	% of barangays with updated data uploaded into the Pagkilos MIS	5. E-governance and data use	SDG 17.18 – Data capacity; SDG 1.5 – Resilience of the poor	Report barangays that completed community risk and vulnerability assessments and successfully entered data	Upload gaps, data quality issues	MIS dashboard reports, community profiling tools, LGU data validation records.

[36] Covered in Chapter 15 of the PDP 2023–2028.
[37] Part of Strategic Focus Area B in the SPP 2023–2028.
[38] Discussed in Chapter 3: Reduce Vulnerabilities and Protect Purchasing Power
[39] Part of Strategic Focus Area C: Rationalization, Modernization, and Integration of the SP System

					into the MIS; mention how data was used in local decision-making.		
Inclusive Economic Recovery and Livelihood Support[40]	Households supported with livelihood/ recovery initiatives[41]	# of households receiving recovery/ livelihood assistance	2. Economic recovery	SDG 8.3 – Jobs and enterprises; SDG 1.4 – Access to services	Number of households (with disaggregation) receiving PCRP-supported interventions like cash-for-work, asset restoration, or microenterprise sub-projects.	Targeting or delivery issues (e.g., overlapping assistance)	Beneficiary lists, fund utilization reports, community operations tracking.
Improved Social Cohesion and Collective Action in Resilience	Strengthened community participation in social protection design and	% of sub-projects assessed as technically/ socially sustainable	5. Participatory development	SDG 16.6 – Accountable institutions	Report results of sustainability assessments based on post-completi	Incomplete assessments or weak O&M mechanisms	Use sustainability checklists, community feedback tools, O&M reports.

[40] Highlighted in Chapter 4: Increase Income-earning Ability.
[41] Aligns with Strategic Focus Area A in the SPP 2023–2028.

Building[42]	implementation[43]	post-completion			on reviews, technical audits, or community monitoring; identify key success factors.		

[42] Part of Chapter 2: Promote Human and Social Development.
[43] Encompassed in the goals of the SPP 2023–2028.

ANNEX H: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) CONTRIBUTIONS TO THE NATIONAL ADAPTATION PLAN 2023-2025[44]

NAP Outcome	NAP Strategy	Description	Project Rationale	Project Indicator	Actual Accomplishment *(What to Report)*	Variance / Gap	Remarks / Notes/ Data Source
Cultural Heritage, Population Displacement, and Migration (DSWD identified as among the implementing lead agencies)							
Outcome 2: Robust preparatory and reintegration support for populations impacted by slow onset climate events	Scale targeted community education programs to increase awareness on climate risks	Establish comprehensive early warning systems to monitor and predict slow onset climate events and combine with targeted community education programs to increase awareness	Pagkilos-PCRP aims to strengthen community capacities for participatory resilience planning and increase resilience investments in vulnerable areas.	No. of communities trained on risk and vulnerability assessment; and, resilience planning	Percentage of communities in covered municipalities with officials, staff or community volunteers were trained on vulnerability assessment and resilient planning		Management Information System

[44] Indicators where DSWD is either an implementing lead agency or supporting agency

		about the potential impacts					
	Facilitate mechanisms for community-based adaptation planning	Facilitate participatory adaptation planning at the community level by collaborating with locals to identify specific vulnerabilities and design context-specific strategies.		No. of communities who have conducted Participatory Risk and Vulnerability Assessment* Not a KPI but still *tracked as part of operations monitoring*	No. of target communities who have completed Stage 1 of the CRIP		Management Information System
Health (DSWD identified as among the supporting agencies)							
Outcome 2: Seamless access to climate-responsive health services underpinned by resilient health networks.	Strengthen WASH protocols and prioritize access to health services in post-disaster and makeshift areas	Scale concrete measures to strengthen water, sanitation, and hygiene and ensure access to health services, given that diseases can be transmitted easily in	The KALAHI-CIDSS PAGKILOS-PCRP aims to strengthen community capacities for participatory resilience planning and increase resilience investments in	Sub-projects completed in accordance with approved technical plans and budget (WASH SPs only)	Percentage of sub projects designed, implemented, and completed in accordance with the approved technical plans and budget.		Management Information System

		post-disaster communities and evacuation centers.	vulnerable areas				

These are indicative contributions based on the National Adaptation Plan (NAP) Stocktaking Workshop held in December 2025, and may be subject to succeeding issuances.

ANNEX I: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) DATA GATHERING AND REPORTING SCHEDULE BY LEVEL

Barangay Level – *Data for Output & Immediate Outcome Indicators*

M&E Tasks	Who are Involved	Reports to be Submitted	Timeline
Installation of Community Monitoring Plans	Community Volunteers (CVs); Community Monitoring Sub Committee (CMSC); Community Facilitator (CEF); Area/Municipal Coordinating Team (A/MCT), and Barangay Officials	Barangay Monitoring Plan; Barangay Profile	Within 7 days after conduct of barangay orientation
Data Collection and Documentation of Activities	CVs (Secretary, Bookkeeper, Treasurer); and Technical Staff: Engineering Forms : Technical Facilitator (TF) Financial Forms: Municipal Financial Analyst (MFA) Process Forms: CFand Area	Activity Minutes Form/Report; Documentation; and relevant CDD forms from the Compendium of Forms	Within 3 days after conduct of activity
Submission of MOVs and Data[45]		MOVs per activity; geotagged photos	Within 5 days after conduct of activity

[45] Includes technical review on completeness, correctness, consistency, and cleanliness of forms.

Official Use Only

M&E Tasks	Who are Involved	Reports to be Submitted	Timeline
	Coordinator (AC) Procurement Forms: ACT and MCT		
Quality Review of MOVs[46]	CVs (Secretary, Bookkeeper, Treasurer); and A/MCT[47]	Validated MOVs Checklist	Within 2 days after submission of MOVs
Geotagging and Monitoring of Sub-projects	TF; Municipal Engineer; and/or any designated staff	Sub-project geotagged photos	During preparation for the request for fund release (RFR); during sub-project (SP) implementation; and 7 days after FIR
Review of community-prepared technical and financial records	CVs; TF and MFA	Technical and Financial Reports	Monthly, 7 days after conduct of activity
BARANGAY-BASED OUTPUTS SCHEDULE			**7 Calendar days**

Municipal Level – *Data Verification and Consolidation for Output & Intermediate Outcome Monitoring*

Tasks	Who are Involved	Reports to be Submitted	Timeline
Data Sharing & Systems Setup	Local Government Unit (LGU), ACT	Data Sharing Agreement;	At the start of the project

[46] Includes provision of technical assistance on the quality of records.
[47] Sectoral review of forms by functional roles of the A/MCT.

Official Use Only

Tasks	Who are Involved	Reports to be Submitted	Timeline
		Memorandum of Agreement (MOA)	engagement
Quality Assurance of Barangay Submissions	Area Coordinator (AC) and Municipal Coordinator (MC)	Inventory & Assessment[48] of MOVs	Within 3 days after receipt of MOVs
Encoding of Paper-Based Reports into MIS	Municipal Data Encoder (MDE) and Project Evaluation Assistant (PEA)	Encoded Data in the MIS	Within 3 days after receipt of paper-based reports
Scanning and digitizing of reports		Inventory of scanned MOVs	1 day after receipt of MOVs
Verification and approval of encoded KPI data in the MIS	TF and MFA[49]; AC and MC	Reviewed KPI data in the MIS	Within 2 days after encoding
Consolidated Municipality Progress Report[50]		Progress Report (KPI, Technical and Financial)	Within 3 days after every cut-off (15th and 30th of month)
Turnover of Reports and Records to LGU	AC and MC; Municipal Resilience Team (MResT); Municipal Planning and Development Coordinator (MPDO) and Local Social Welfare and Development Officer (LSWDO)	Report Acceptance Certificate	End of project cycle

[48] Status on quality, quantity, and timeliness
[49] Verification, approval and checking of MIS data for technical and financial forms
[50] Includes analysis of KPI, technical and financial data in the MIS, and report processing

Official Use Only

Tasks	Who are Involved	Reports to be Submitted	Timeline
Assist technical staff in the operation of the MIS and the implementation of the data collection system	MDE and PEA	Minutes of the Meeting (MoM)	Start, mid-term, end of project As need arises
MUNICIPAL-BASED OUTPUTS SCHEDULE			**3-7 Calendar Days**

Regional Level – *Oversight and Aggregation for Intermediate and Higher-Level Outcomes*

Tasks	Who are Involved	Reports to be Submitted	Timeline
Regional Technical Assistance & Coaching[51]	Project Evaluation Officers (PEOs) and Regional Team[52]	Training Report; TA Report; Regional Coaching Feedback Report	Start, mid-term, end of project As need arises
Verification, checking, and approval of KPI, technical and financial data in the MIS	PEOs and Regional Team	Reviewed KPI, technical and financial data in the MIS	Within 2 days after encoding
Generation and processing of KPI, technical and financial data from the MIS	PEOs	Consolidated KPI, technical and financial reports from the MIS	Within 2 days after every cut-off (15th and 30th of the month)
Regional Consolidation of	PEOs and Regional Team	Regional KPI Status Report; Thematic	Within 5 days after every cut-off (15th

[51] Provision of technical assistance, support, and troubleshooting for MIS operations
[52] Community Development Officer, Infrastructure Officer, Procurement Officer, and Financial Analyst

Official Use Only

Tasks	Who are Involved	Reports to be Submitted	Timeline
Reports[53]		Reports; Progress Report	and 30th of month)
Data Quality Assessment (DQA) and Desk Review[54]	Regional Team; PEOs	DQA report; Consolidated DQA Narrative Report	Monthly, 3 days after end of the month
Submission of Regional Regular Reports	Regional Team; PEOs; Training Specialist (TS); Social Marketing Officer (SMO)	Quarterly, Semestral, Annual Statistical and Narrative Reports; Safeguards and GAD Reports; Physical Progress Report; Procurement Monitoring Report; Financial Report; CapBuild Report; Communication and Advocacy Report	5th day of the succeeding month/quarter
Review and Endorsement to National	Deputy Regional Program Manager (DRPM); Regional Program Manager (RPM); and Regional Director (RD)	Endorsed Regional Technical Reports	8th day of the succeeding month/quarter
REGIONAL-BASED OUTPUTS SCHEDULE			**8 Calendar Days**

National Level – *Strategic Monitoring, Evaluation, and Policy Feedback*

[53] KPI, process, technical and financial reports
[54] Conduct of desk reviews and quality checks of the MIS data, with provision of feedback

Official Use Only

Tasks	Who are Involved	Reports to be Submitted	Timeline
Provision of technical assistance, support, and troubleshooting for MIS operations	Program Compliance Division	Training, Feedback or Coaching Report	Start, mid-term, end of project As need arises
Generation and processing of KPI, technical and financial data from the MIS	Program Compliance Division	Consolidated KPI, technical and financial reports from the MIS	Within 3 days after every cut-off (15th and 30th of the month)
Verification, checking, and approval of KPI, technical and financial data in the MIS[55]	Program Compliance Division	Reviewed KPI, technical and financial data in the MIS; Consolidated KPI dashboard; MIS Feedback Notes	Within 3 days after issuance of MIS report
Data Quality Assessment (DQA) and Desk Review[56]	All sectors; Regional PEOs and Program Compliance Division	DQA and Thematic Review Reports; Consolidated DQA Narrative Report	Semestral, 7-days after end of the reporting period
Submission of Technical Reports	All sectors; Program Compliance Division	Quarterly, Semestral, Annual Statistical and Narrative Reports; Safeguards and GAD Reports; Physical Progress Report; Procurement Monitoring Report;	8th day of succeeding month/quarter

[55] Including analysis of KPI and thematic trends
[56] Cross-sectoral Desk Reviews

Official Use Only

		Financial Report; CapBuild Report; Communication and Advocacy Report	
Approval of Technical Reports	Deputy Program Managers; National Program Manager	Technical Progress Reports	10th day of the succeeding month/quarter
NATIONAL-BASED OUTPUTS SCHEDULE			**10 Calendar Days**

Official Use Only

ANNEX J: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) DATA GATHERING ACTIVITIES, SOURCES, AND INFORMATION BY IMPLEMENTATION LEVEL

Level	Data Gathering Activities	Data Sources	Information Collected / Used
Community / Barangay	- Coordination with PB and MPDC - Review of BDP, BDIP, AIP, and BNAP, DRR Plan - Participatory Risk, Vulnerabilities, and Capacity Assessment (PSA) - SP implementation monitoring - SFM tracking - Geotagging of SPs - Preparation of SP completion reports	- Barangay Profiles - Community-Based Monitoring System (CBMS) - Registry of Barangay Inhabitants (RBI) - PSA materials and participatory tools - CDRA results - BDC, BDRRMC, community volunteers - Official barangay and MLGU databases	- Existing and updated barangay data - Priority SPs and programming criteria - CRSPMC composition - SP approvals (resolutions, C/MRPs, Multi-year Plans) - Sectoral planning data tables - Participation and implementation quality - Stakeholder Feedback - SP completion and accountability reports

Official Use Only

Level	Data Gathering Activities	Data Sources	Information Collected / Used
Municipal	- Collection and filing of profiles, Stakeholder Feedback, SET - Facilitation of MOA and SIA compliance -MResT Meetings - Data gathering from municipal departments - Oversight of SP delivery and compliance	- LGU records and planning documents - MOA and MResT resolution - Municipal LGU departments - RPMO coordination	- LGU development priorities - MOA implementation provisions - MResT TA support plans - MResT technical certifications and SP endorsements - National and provincial validation data - Stakeholder Feedback intake logs
Regional / National	- Spot checks and TA by RPMO - Consolidation of municipal and regional reports - Coordination with NGAs - Handling of national-level grievances - Monitoring convergence activities	- RPMO monitoring reports - National government agency databases - Pagkilos plans - DSWD SFM	- Regional/ provincial development commitments - Gaps and opportunities for local development - Consolidated findings from lower levels - Data for national policy guidance and convergence efforts

Official Use Only

ANNEX K: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) REPORTING FORM REQUIREMENTS

Seq	Activities	Expected Outputs	M&E Form/Tool
		STAGE 1	
1	Municipal Orientation	Signed Memorandum of Agreement (MOA) • Inclusive of Data Sharing Agreement Approved Executive Order forming the: 1. Municipal Resilience Team (MResT) 2. Municipal Coordinating Team (MCT); and 3. Grievance Redress Team (GRT) Schedule for the PRVA	• Municipal Activity; Attendance Sheet; • Municipal Activity Minutes Form
2	First Barangay Assembly	Approved Barangay Development Council (BDC) resolution indicating the list of the following: 1. Identification of Community Volunteers for the mapping of needs 2. Minimum rate of participation in barangay assembly	• Barangay/Community Assembly Attendance Sheet • Barangay Activity Minutes Form Attachments • Resolution • Barangay/Community Household Participation • CV Profile Form
3	Participatory Risk and Vulnerability Assessment	Sub Activity 1: Accomplishing the community profile • Draft Community Profile Sub Activity 2: Community Walkthrough • CV's notes[57] Sub Activity 3: Community Mapping • Draft Community Map (may be physical map or accomplished through the MIS) Sub Activity 4: Focused Group Discussion • Accomplished FGD Template Sub Activity 5: BRVA Workshop • Finalized Community Profile and Map	• Barangay/Community Meeting/Training Attendance Sheet • Barangay Activity Minutes Form Attachments • Community Profile • Community Map

[57] To be used as reference during the succeeding sub activities i.e. Community Mapping, etc.

Official Use Only

4	Municipal Resilience Planning and Prioritization of PPAs for PCRP Funding (Multi-Year Planning)	Approved Municipal Resilience Plan (MRP) indicating the Pagkilos list of funded interventions (multi-year plan) with indicative costs Approved SP Clustering Process (if applicable) Developed Criteria for Resource Allocation	• Municipal Activity Attendance Sheet • Municipal Activity Minutes Form[58] Attachments • Municipal Resilience Plan
5	Barangay Development Council Meeting: Feedbacking of MRP Result, Resource Accessing and Selection of CSPMC, PPSC and O&MSC (year 2 and 3 prioritized barangays)	Approved BDC resolution affirming the MRP Result, and designating the members of the CPMC, PPSC, and O&MSC	• Barangay/Community Meeting/Training Attendance Sheet • Barangay Activity Minutes Form Attachments • Resolution
6	RPMO Appraisal of Municipal Resilience Plan	Accomplished appraisal of the MRP (to be prepared by the RPMO)	
STAGE 2			
7	Second Barangay Assembly: Section of CSPMC, Planning for SP Implementation and Concept Note Development (for prioritized barangays)	Approved resolution designating the members of the CSPMC	• Barangay/Community Meeting/Training Attendance Sheet • Barangay Activity Minutes Form Attachments • Resolution
8	Training for Community Sub-Project Management Committees (CSPMC)	Developed action plans based on the capacity-building activities attended.	
9	Sub Project Development Workshop	Prepared detailed estimates and plans, procurement packages, Environmental and Social Management Plan (ESMP) and draft project proposal	• Municipal Activity Attendance Sheet • Municipal Activity Minutes Form • SP's Household Beneficiaries
10	Third Barangay Assembly: Presentation and Approval of Community Resilience Sub Project Proposal	Approved resolution endorsing the full-blown proposals to the MResT for Technical Review and request endorsement for Pagkilos funding	• Barangay/ Community Assembly Attendance Sheet • Barangay Activity Minutes Form Attachments • Resolution • Barangay/Community Assembly Household Participation
11	MResT Technical Desk Review	Passed resolutions endorsing and approving the proposal for	• Municipal Activity Attendance Sheet

[58] Mentions the approved SP Clustering Process and criteria for resource allocation

Official Use Only

		Pagkilos funding, basis for the obligation of funds	• Municipal Activity Minutes Form Attachments • Resolution
12	Processing and Release of Grants and Subsidies	Downloaded Community Grants/subsidy to the community account	*Refer to SM4: Community-Level Financial Management*
13	Formation of Operation and Maintenance Group	Organized O&M Group and MSIT	• CV Profile Form
STAGE 3			
14	Community-Based Training Workshop for Community Volunteer	Trained Community Volunteers	• Municipal Activity Attendance Sheet • Municipal Activity Minutes Form • CV Profile Form
15	Community Procurement	Procured goods and supplies for SP implementation	*Refer to SM6: Community-Managed Procurement*
16	Sub Project Implementation	Completed SPs in accordance with set standards and specification	• Sub-Project Workers Basic Profile • SP's Household Beneficiaries
17	Operation and Maintenance Workshop	Trained O&M Group	• Municipal Activity Attendance Sheet • Municipal Activity Minutes Form
18	BDC Meeting: Approval of the 2nd and Final Tranche Request	Approved 2nd and final tranche	• Barangay/ Community Meeting/ Training Attendance Sheet • Barangay Activity Minutes Form
STAGE 4			
19	Barangay Accountability Reporting	Approved commitment plan and resolution on the continuous funding of Resilient Programs, Project and Activities (PPAs)	• Barangay/ Community Meeting/ Training Attendance Sheet • Barangay Activity Minutes Form Attachments • Resolution • Commitment Plan
20	Closing Activities • Closing of Account • Booking of Assets • Completion of the SPCR • Functionality Audit • Project Turnover	Closed account and approved SPCR	• Sub Project Completion Report

Official Use Only

21	Fourth Barangay Assembly: Final Feedbacking and Reporting	Approved exit plan covering the sustainability arrangement and monitoring plan of the unfunded Programs, Projects, and Activities	• Barangay/ Community Assembly Attendance Sheet • Barangay/Community Assembly Household Participation • Barangay Activity Minutes Form Attachments • Exit Plan
22	Municipal Sustainability and Accountability Reporting (Year 3)	Approved Municipal Sustainability Plan and Resolution on the continuous funding of Resilient PPAs (MAR will be conducted in the last year of the implementation in the municipality	• Municipal Activity Attendance Sheet • Municipal Activity Minutes Form Attachments ○ Sustainability Plan ○ Resolution
Across Community Resilience Implementation Process (CRIP) Stages			
a. Stakeholder Feedback Mechanism (SFM) Intake Form b. SFM Installation Checklist c. Oversight and Coordinating Committees Checklist d. Participatory, Transparency, and Accountability (PTA) Integration Checklist			

Official Use Only

ANNEX L: PHILIPPINE COMMUNITY RESILIENCE PROJECT (PAGKILOS) COMMUNITY MONITORING TOOLKIT

I. Introduction to Community Monitoring in PCRP

Community Monitoring (CM) under the *Philippine Community Resilience Project (Pagkilos)* is a participatory process where community members track, validate, and assess the implementation of their Community Resilience Plans (CRPs). It empowers communities to take ownership of their development and resilience-building efforts.

Following the action-reflection-action framework, Community Monitoring promotes adaptive learning and local accountability. It supports the core principles of PCRP: inclusive governance, systems resilience, and strengthened citizen engagement.

II. Objectives of Community Monitoring

- Ensure the timely and appropriate implementation of CRP activities and funded sub-projects.
- Assess the fulfillment of community and LGU commitments.
- Capture challenges and enabling factors in CRP implementation.
- Facilitate collective reflection and improve resilience programming.
- Generate community evidence for decision-making and Barangay Accountability Reporting (BAR).

III. Who Participates in Community Monitoring?

1. **Community Monitoring Sub Committee (CMSC)** – The CMSC is formed later in the process, with its members selected from among the representatives from different sitios/purok who make up the *Barangay Resilience Team (BResT)*. It is a group of community members tasked with tracking the progress, compliance, and effectiveness of program activities. They ensure transparency,

Official Use Only

accountability, and community engagement by monitoring project implementation, performance indicators, and adherence to environmental and social safeguards.

CMSC Functions:

a. Monitor the implementation and ensure compliance with the plans and activities of all community teams under the CRSPMC.

b. Track the community's progress and adherence to the Key Performance Indicators (KPIs) at the Barangay Level.

c. Act as the advocacy arm of the program, promoting awareness and support for its goals and initiatives.

d. Oversee the implementation and monitoring of the Environmental and Social Management Plan (ESMP).

The CMSC is composed of at least three (3) Community Volunteers (CVs) elected by the Barangay Assembly (BA)

2. **Municipal Resilience Team (MResT)** – Provides technical support and coordinates with LGUs.
3. **LGU Representatives** – Contribute data and validate implementation.
4. **Other Stakeholders** – Community-based organizations, CSOs, sectoral groups.

IV. Activities and Timeline

Activity	When	Details
Selection of CMSC members and Orientation	2nd Barangay Assembly (BA)	• BResT volunteers will become CM Volunteers, subject to the approval of theCRSPMC and the concurrence of the BDC.) • Chairperson selected among the

Official Use Only

		CM Volunteers
Monitoring Plan Development and Work Plan Preparation	1 week after Community Resilience Planning	• Based on the CRP, the team identifies what to monitor, and prepares the Monitoring Plan • Prepare Work Plan: Assign tasks, define methods, prepare logistics.
Approval of Plans	Community Validation Session	The community endorses what and how to monitor.
Midterm Monitoring & Reflection	After Municipal Resilience Planning and Prioritization of PPAs	Field monitoring, validation meetings, data collection.
Mid-Cycle Reporting	One week after midterm monitoring	Discuss midterm findings with stakeholders.
Final Monitoring & Reporting	End of RAP Implementation	Document performance, gaps, and lessons.
Barangay Accountability Reporting	Final community assembly	Present findings, and solicit feedback

Official Use Only

V. Monitoring Plan Template (Sample)

Barangay: San Isidro
Municipality: Sta. Maria
Province: Camarines Sur
Monitoring Period: January – June 2025

Monitoring Area	Key Activities	Expected Outputs / Beneficiaries	Sources of Information	Midterm Accomplishment	Endline Accomplishment	Remarks / Insights
CRP Implementation	Tree planting along riverbanks	1,000 trees planted / 200 HHs	RAP tracker, ocular visits	600 trees planted	1,100 trees planted	Surpassed target due to strong youth participation
Community Commitments	Barangay funds for tools	PHP 10,000 disbursed	Barangay records, minutes	PHP 5,000 disbursed	PHP 10,000 disbursed	Full LGU commitment achieved
LGU Technical Support	DRR training sessions	3 trainings / 90 pax	Attendance sheets, photos	2 sessions completed	3 sessions completed	Include health resilience in future modules

Sub-project Delivery	Multipurpose hall retrofitting	Facility functional / 300 HHs	SPCR, photos, household interviews	50% done	Completed	Delay due to procurement; caught up after LGU stepped in

VI. Work Plan Template (Sample)

Barangay: San Isidro
Monitoring Cycle: January – June 2025

Major Activity	Specific Task	Schedule	Persons Involved	Resources Needed
Midterm Monitoring	Ocular visit to tree planting sites	March 2025	CMVs, BRF	Transportation, camera
	Interview with barangay officials	March 2025	CMV Chair, BRF	Questionnaire
	RAP implementation progress review	March 2025	CMVs	RAP Tracker, minutes
Endline Monitoring	Sub-project site inspection	June 2025	CMVs, MRF	PPEs, camera
	Community feedback session	June 2025	CMVs, BRF, LGU	Sound system, venue
Data Analysis & Report	Consolidation & validation workshop	June 2025	CMVs, BRF	Laptop, report template

VII. Data Gathering Guide (Sample)

Area of Monitoring	Information Needs	Source	How to Get Info	Who Can Help?
RAP Activities	Activity completion status	RAP Tracker	Review documents, ocular	BRF, CMVs
LGU Commitments	Budget releases, technical inputs	MOAs, barangay files	Interview, review records	MRF, Barangay Secretary
Sub-project Implementation	Physical and financial progress	SPCR, contractor	Inspection, reports	LGU Engineer, ACT
Participation/Inclusion	Attendance and feedback	Activity sheets	FGDs, key informant interviews	CMVs, Sectoral Groups

VIII. Data Analysis & Reporting

1. Validate data completeness and accuracy.
2. Group data per monitoring area and timeline.
3. Triangulate – compare sources for consistency.
4. Interpret patterns, bottlenecks, and unexpected results.
5. Document both quantitative results and qualitative insights.
6. Prepare Presentation for BAR using posters, summary tables, and testimonies.

IX. Barangay Accountability Reporting (BAR)

The CMVs facilitate the end-of-cycle presentation of findings. This session:

- Reviews the accomplishments and gaps.
- Involves LGUs, sectoral groups, and the community.
- Identifies areas for improvement and actions for the next RAP cycle.
- Documents lessons for the Municipal Resilience Learning Session

Official Use Only

ANNEX M: RESEARCH AND EVALUATION AGENDA

The Philippine Community Resilience Project (Pagkilos) aims to enhance the adaptive capacity of vulnerable communities and ecosystems to natural hazards and emerging risks resulting from Climate Change. Its development objective is to *strengthen community capacities for participatory resilience planning and increase resilience investments in vulnerable areas*. To gauge the accomplishment of the development objective, the following Key Performance Indicators (KPIs) will be used:

a. Percentage of beneficiaries reporting that they can influence community resilience planning;
b. Percentage of target municipalities with community-led resilience plans integrated in their Comprehensive Development Plan (CDP); and
c. Population in target areas benefiting from resilience investments.

Pagkilos also aligns with the Philippine Development Goal to achieve economic and social transformation for a prosperous, inclusive, and resilient society, and is congruent with the Adaptive Shock Responsive Roadmap[59]. Relatedly, the Pagkilos is aligned with the country's commitment to the Sustainable Development Goals (SGDs) and will contribute in the following areas[60]:

SDG 1: No Poverty
SDG 2: Zero Hunger
SDG 6: Clean Water and Sanitation
SDG 8: Decent Work and Economic Growth
SDG 9: Industry, Innovation, and Infrastructure
SDG 11: Sustainable Cities and Communities
SDG 13: Climate Action

The project contributes to the accomplishment of the National Adaptation Plan (NAP) which seeks to address the country's vulnerability to climate change and its adverse impacts. The Pagkilos is aligned with the NAP strategy which recognizes the need to empower local governments and communities to take adaptive action[61]

Research and Evaluation Agenda

[59] As outlined in Chapter 3.2 of the PDP 2023-2028
[60] "THE 17 GOALS | Sustainable Development," accessed April 26, 2025, https://sdgs.un.org/goals.
[61] "National Adaptation Plan of the Philippines 2023-2050," n.d., 160.

Official Use Only

The Research and Evaluation Agenda serves as a framework for: 1.) generating critical knowledge to support project implementation; 2.) providing insight for further refining CDD as a development approach; and 3.) providing data-driven and empirical support for the CDD advocacy and its institutionalization.

This agenda comprises six (6) priority studies throughout the five (5) year implementation of the PCRP. These primary studies are to be conducted externally by consulting firms or consultants procured. Although, additional studies may be proposed (which may be conducted internally or externally) as needed and approved by the NPMO subject to applicable guidelines of the DSWD.

Year	Study
Year 1 - 2026	Baseline Study
Year 2 - 2027	Special / Thematic Study
Year 3 - 2028	Midline Study
	Special / Thematic Study
Year 4 - 2029	Special / Thematic Study
Year 5 - 2030	Endline Study

These priority studies consist of three (3) periodic studies, namely the baseline, midline and endline studies, and three (3) special / thematic studies.

Periodic Assessments

Periodic studies, consisting of the baseline, midline, and endline studies, will measure the accomplishment of project development outcomes. As detailed in the hierarchical relationship of indicators, these indicators directly contribute to the accomplishment of project development outcome. Program implementation (as monitored through intermediate indicators which correspond to the 3 Pagkilos components) directly impacts the project development outcomes.

Official Use Only

Baseline, midline, and endline studies, as their name implies, will assess project development outcomes before, during, and after project implementation. Specifically,


- *Establish baseline, midline, and endline values for Key Performance Indicators (KPIs) under Project Development Outcomes (PDOs).* Having comprehensive and detailed pre-, during, and post- project measurements of PDOs can provide a reference or point of comparison to evaluate progress being made during project implementation

- *Assess current institutional capacities of Local Government Units (LGUs) in resilience planning and implementation.* The study identified the most vulnerable municipalities in terms of poverty incidence in relation to climate risks, stunting, and IP population. From this, the study will provide a comprehensive assessment of these municipal LGUs to identify facilitating and hindering factors in creating and implementing policies for promoting resilience and reducing climate risk.

- *Identify existing vulnerabilities to natural hazards.* It follows that these municipalities would also have communities among the most vulnerable to natural hazards. As such, the study will also seek to provide a comprehensive assessment of community vulnerabilities to natural hazards and how these may be exacerbated with other vulnerabilities pertaining to gender, indigeneity, disability, and age.


- *Provide recommendations on project interventions and implementation strategies.* The study will provide insight that may inform decisions and steering measures to be made by the NPMO, and/or for future KALAHI-CIDSS modalities.

Official Use Only

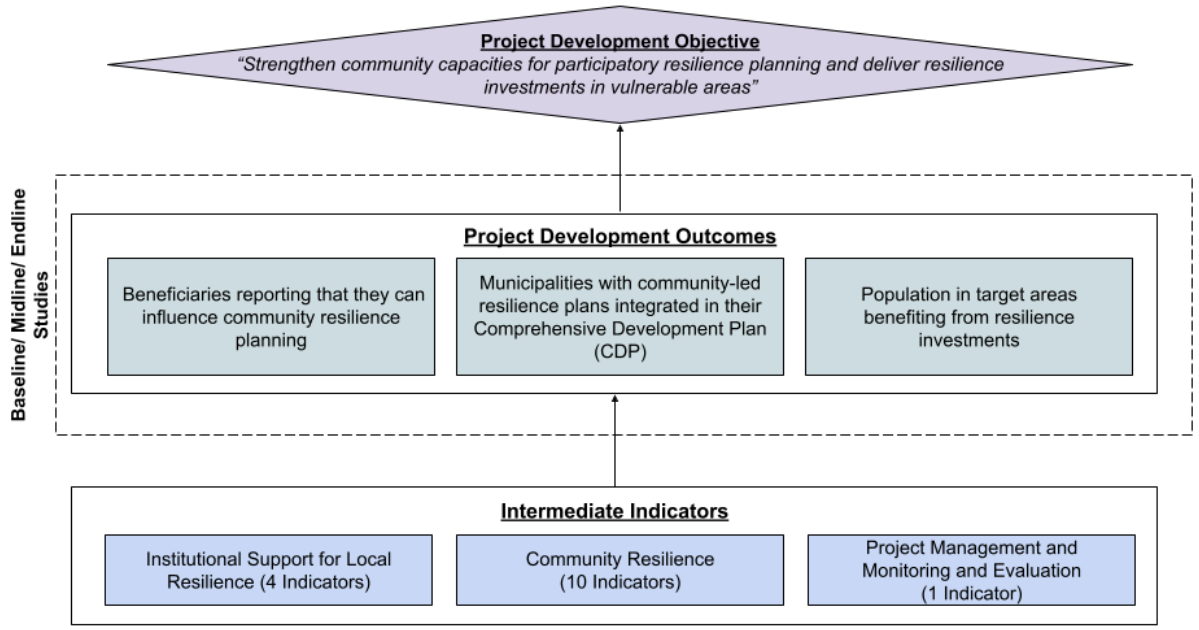

Special / Thematic Studies

Special/Thematic Studies have a specific focus and/or conducted during key points in the project cycle. The specific focus and design of these studies are to be determined during project implementation, responsive to program needs, and informs the strategic direction being taken.



Operations Monitoring and Gap Identification

Project Monitoring tracks activities and deliverables to verify whether they are being executed according to approved work plans, operational guidelines, schedules, technical standards, or as to commitments made. Plans are subject to change and/or adjustments in response to operational realities and emerging obstacles. The extent to which unforeseen challenges affect project implementation is dependent on the preparations or precautions made, as well as the competence of those responsible. The NPMO will interpret patterns, bottlenecks, and unexpected results from RPMO reports to identify aspects

Official Use Only

requiring deeper investigation. Potential topics for Special/Thematic Studies are informed by:

- Strategic Assumptions:
    - Seeks to identify hindering and enabling factors in accomplishing the project's KPIs, in accordance with the schedule planned in the Indicator Tracking Table (ITT).
- Implementation Realities:
    - Certain concerns may be raised that need to be addressed by the RPMO and NPMO during the course of implementing the CRIP. Should these be recurring issues or common across multiple areas, these concerns would be policy in nature - needing to be addressed at an institutional level.
- Institutional Capacity Needs:
    - Gaps may occur at an institutional level. The NPMO and RPMO, as project implementers, may also identify supply side (inputs) needs (i.e. lack of manpower, training, etc.) and/or bottlenecks that hinder delivery of commitments.

Joint Agenda Setting and Study Conceptualization

The KALAHI-CIDSS NPMO and World Bank will collaborate and jointly explore possible research topics. This collaboration ensures that the proposed special/thematic studies are strategically aligned with both national development plans and international best practices for climate change adaptation. Following a series of exploratory meetings, the NPMO will prepare the concept note and terms of reference for the conduct of the study - which takes into consideration the technical recommendations raised.

Processing of Pre-requisite Approvals and Procurement

The Concept Note (and other applicable pre-requisite documents) will undergo through the following:

- Review of the Policy Development and Planning Bureau (PDPB) in accordance with the department policies on research and evaluation
- Review and issuance of a No Objection Letter (NOL) from the World Bank

Official Use Only

- Review in accordance with procurement processes
- Review by the Philippine Statistics Authority (PSA) through the Survey Review and Clearance System (SSRCS) as mandated by RA 10625.

Study Implementation

The KALAHI-CIDSS NPMO will closely monitor the implementation of the study. Validity of findings is contingent on the execution of methodology and tools as intended. Deviation from established protocols - whether through inconsistent application of measurements, improper participant enrollment, etc. - introduces confounding circumstances that may skew the final analysis. Relatedly, there is also a need to ensure that the rights of the study participants as data subjects are upheld and are not violated during their participation. Close monitoring is essential against procedural drift, data contamination,

Presentation of Findings and Recommendation

Depending on the scope of the ToR, the completed write-up of the special/thematic study will be prepared by either the procured research team or by the NPMO. Should the analysis and writing of the completed study be contracted to a research team or firm, the said team or firm will present the findings of the special/thematic study to the KALAHI-CIDSS NPMO and the World Bank. Should the completed write-up be prepared jointly by personnel at the KALAHI-CIDSS NPMO and consultants at the world bank, the NPMO and World Bank are to meet to jointly discuss the findings and recommendations of the study.

Official Use Only

ANNEX N: DECLARATION AND DATA CONSENT FORM

DECLARATION AND DATA CONSENT FORM


☐ I allow DSWD to process my personal information in a manner that ensures appropriate privacy and I declare that: all information in this application are true and correct to the best of my personal knowledge; and all records submitted to the Department of Social Welfare and Development (DSWD) are authentic. The submission of any false or misleading information, or forged/falsified documents, shall be sufficient ground for appropriate legal action against me.

☐ I hereby affirm my rights as a data subject, pursuant to the provisions of Republic Act No. 10173 (Data Privacy Act of 2012) and its Implementing Rules and Regulations:

g. Right to be informed;
h. Right to object;
i. Right to access;
j. Right to rectification
k. Right to erasure or blocking; and
l. Right to damages.

_____
SIGNATURE OVER PRINTED NAME
Date: _____

Official Use Only

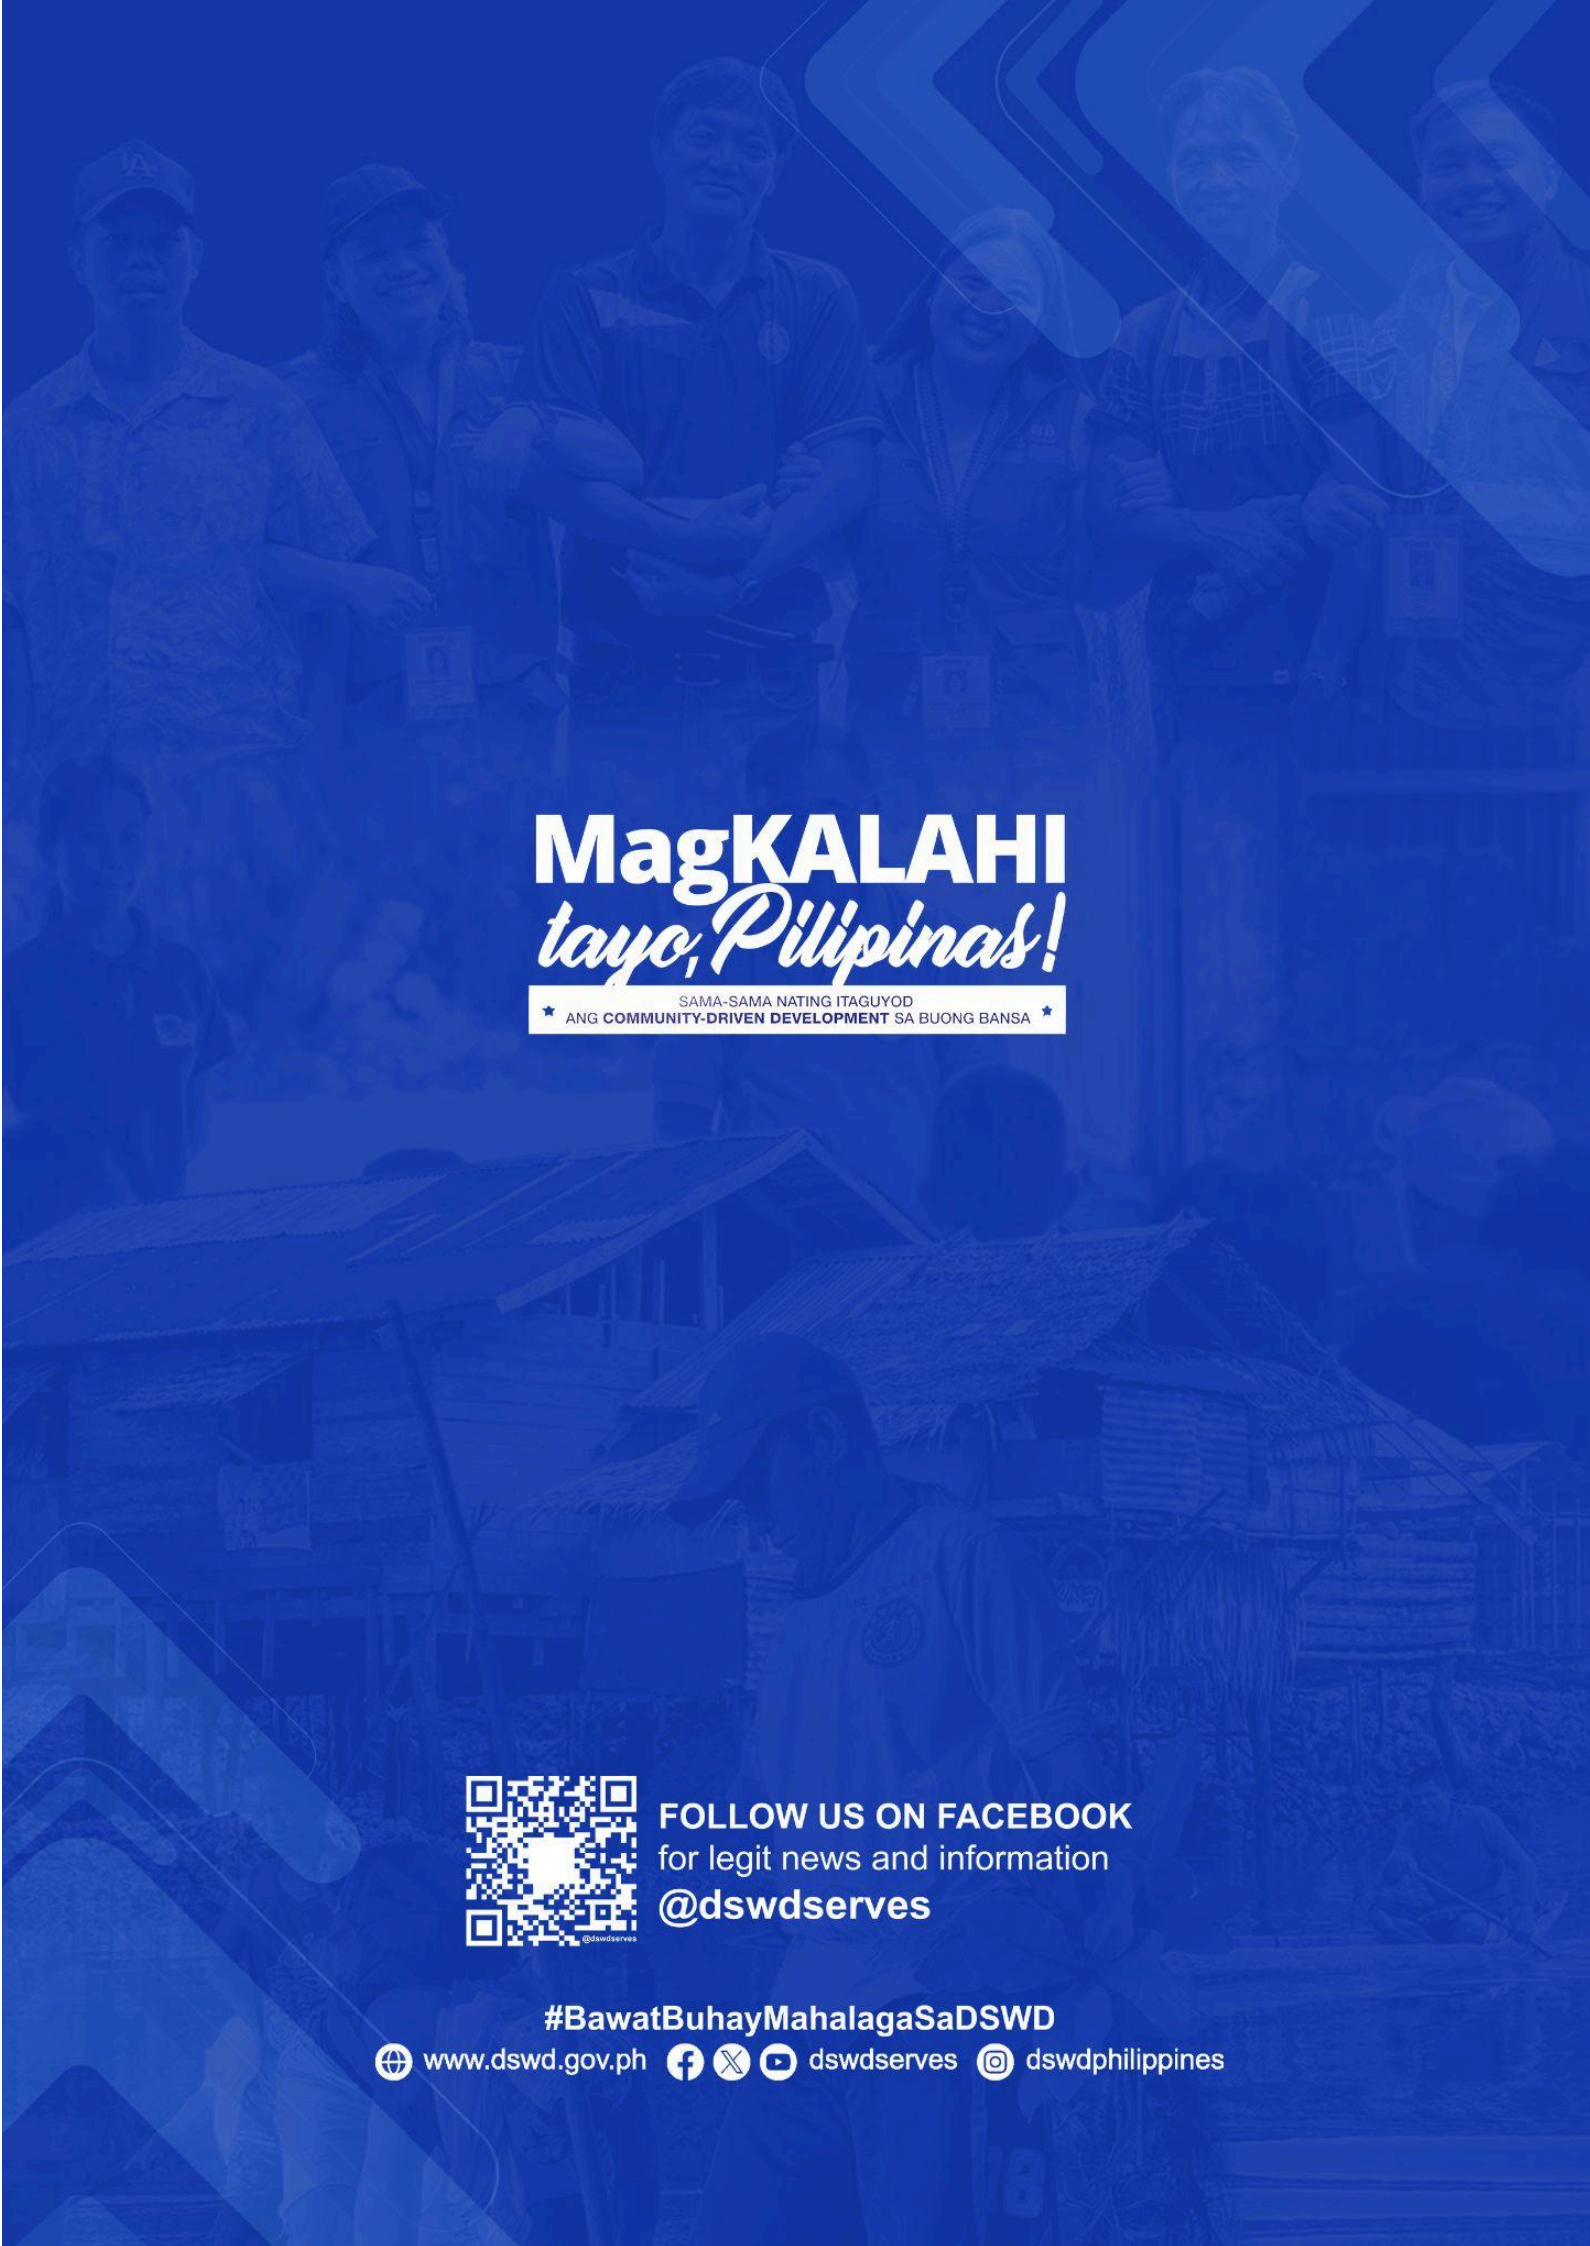
MagKALAHI
tayo, Pilipinas!
SAMA-SAMA NATING ITAGUYOD
ANG COMMUNITY-DRIVEN DEVELOPMENT SA BUONG BANSA
FOLLOW US ON FACEBOOK
for legit news and information
@dswdserves
#BawatBuhayMahalagaSaDSWD
www.dswd.gov.ph
dswdserves
dswdphilippines
